

MCB Quantico Marsh Center Testing Statistics

		Terminated on Panels	Tested	Pass	Fail	Marginal		Tested	Pass	Fail	Marginal	
East Closet Voice		139	121	89	27	5		87.05%	73.55%	22.31%	4.13%	
East Closet Data		276	249	205	37	7		90.22%	82.33%	14.86%	2.81%	
West Closet Voice		156	142	93	46	3		91.03%	65.49%	32.39%	2.11%	
West Closet Data		312	279	238	39	2		89.42%	85.30%	13.98%	0.72%	
		883	791	625	149	17		89.58%	79.01%	18.84%	2.15%	
Cables Not Identified		92										

East Side

(27) Biscuits/Bezels not attached to furniture

West Side

(32) Biscuits/Bezels not attached to furniture


Recommendations:

- 1) Properly measure the cut out openings in the cubicle furniture and install a bezel that matches the opening size
- 2) Replace all jacks at the station side of the cabling and retest. This will ensure all are equal quality and terminated correctly
It will also correct all of the failing/broken jacks.
- 3) Consider an overhaul of the telecom rooms. (See Telecom room overservations)

Additional drop locations needed
per Mike Elliott (NEED APPROVAL TO INSTALL) changes total from 270 to 273

SINGLE WORK STATION LOCATION – 3
CAT6 JACKS/DROPS EACH

TOTAL OF 270 WORK STATION
LOCATIONS – 810 CAT6 JACKS/DROPS

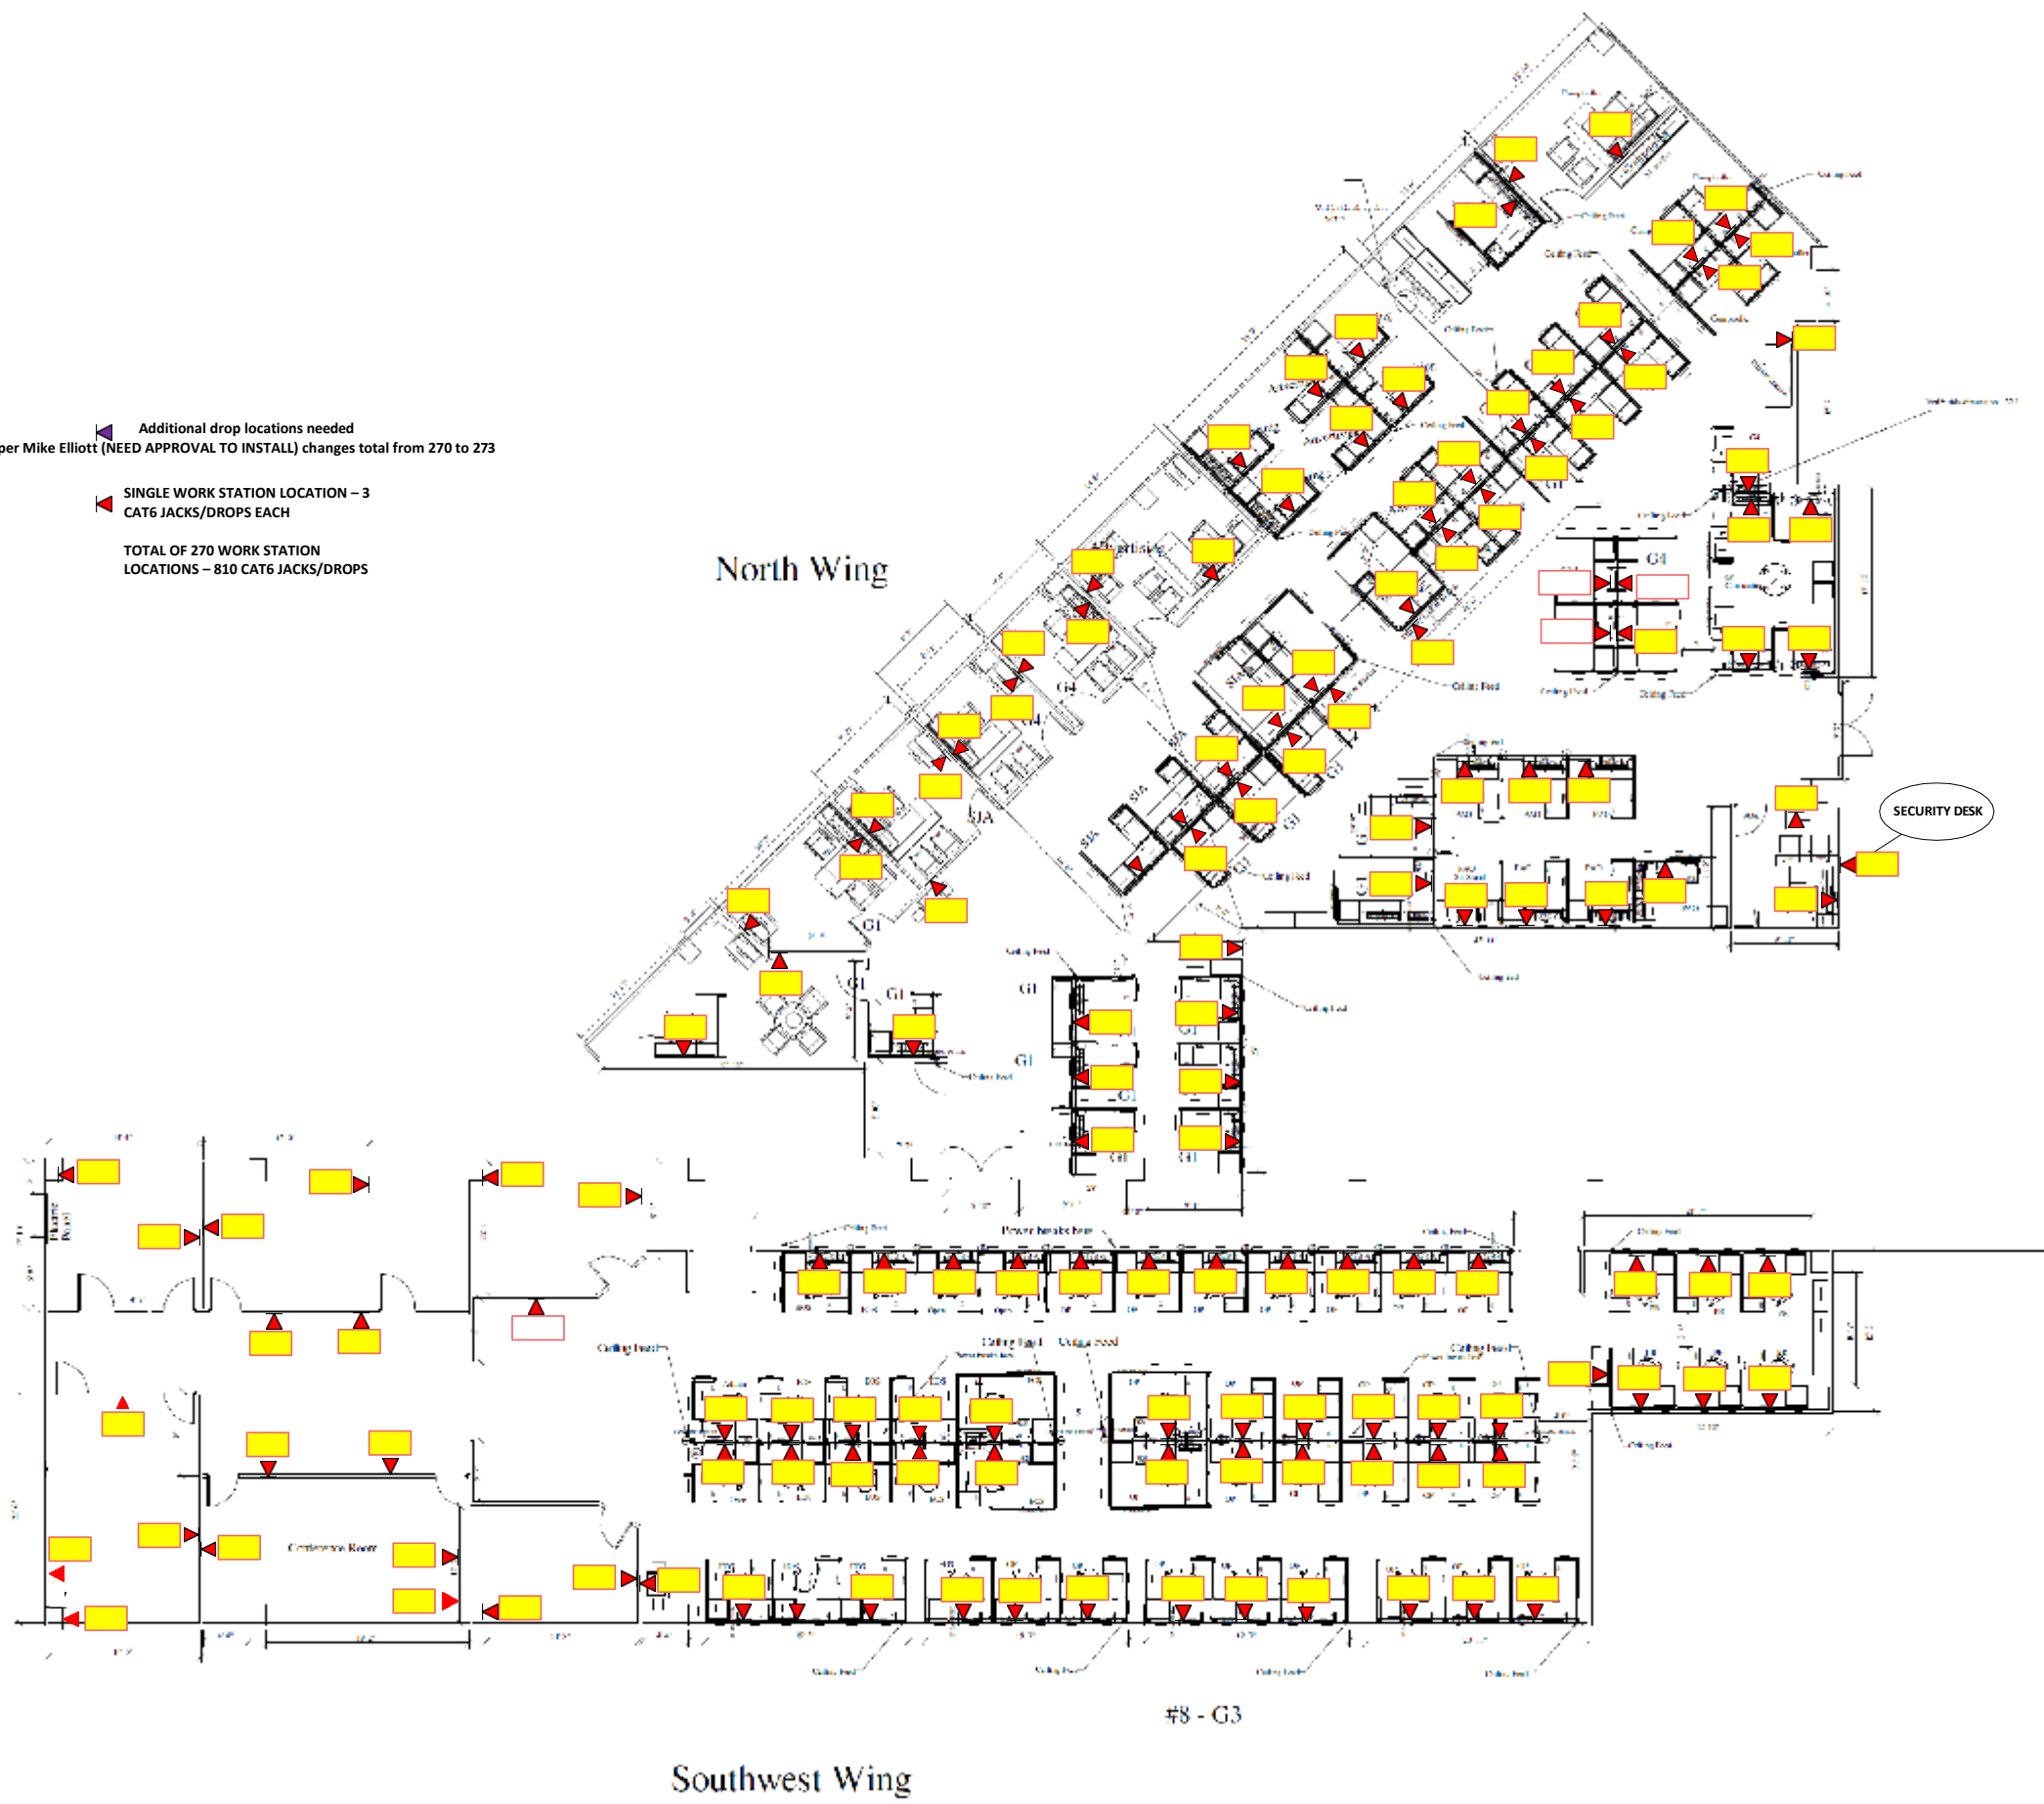


USMC Marsh Center

2nd Deck

Recruiting Command HQ

South/East Telecom Room

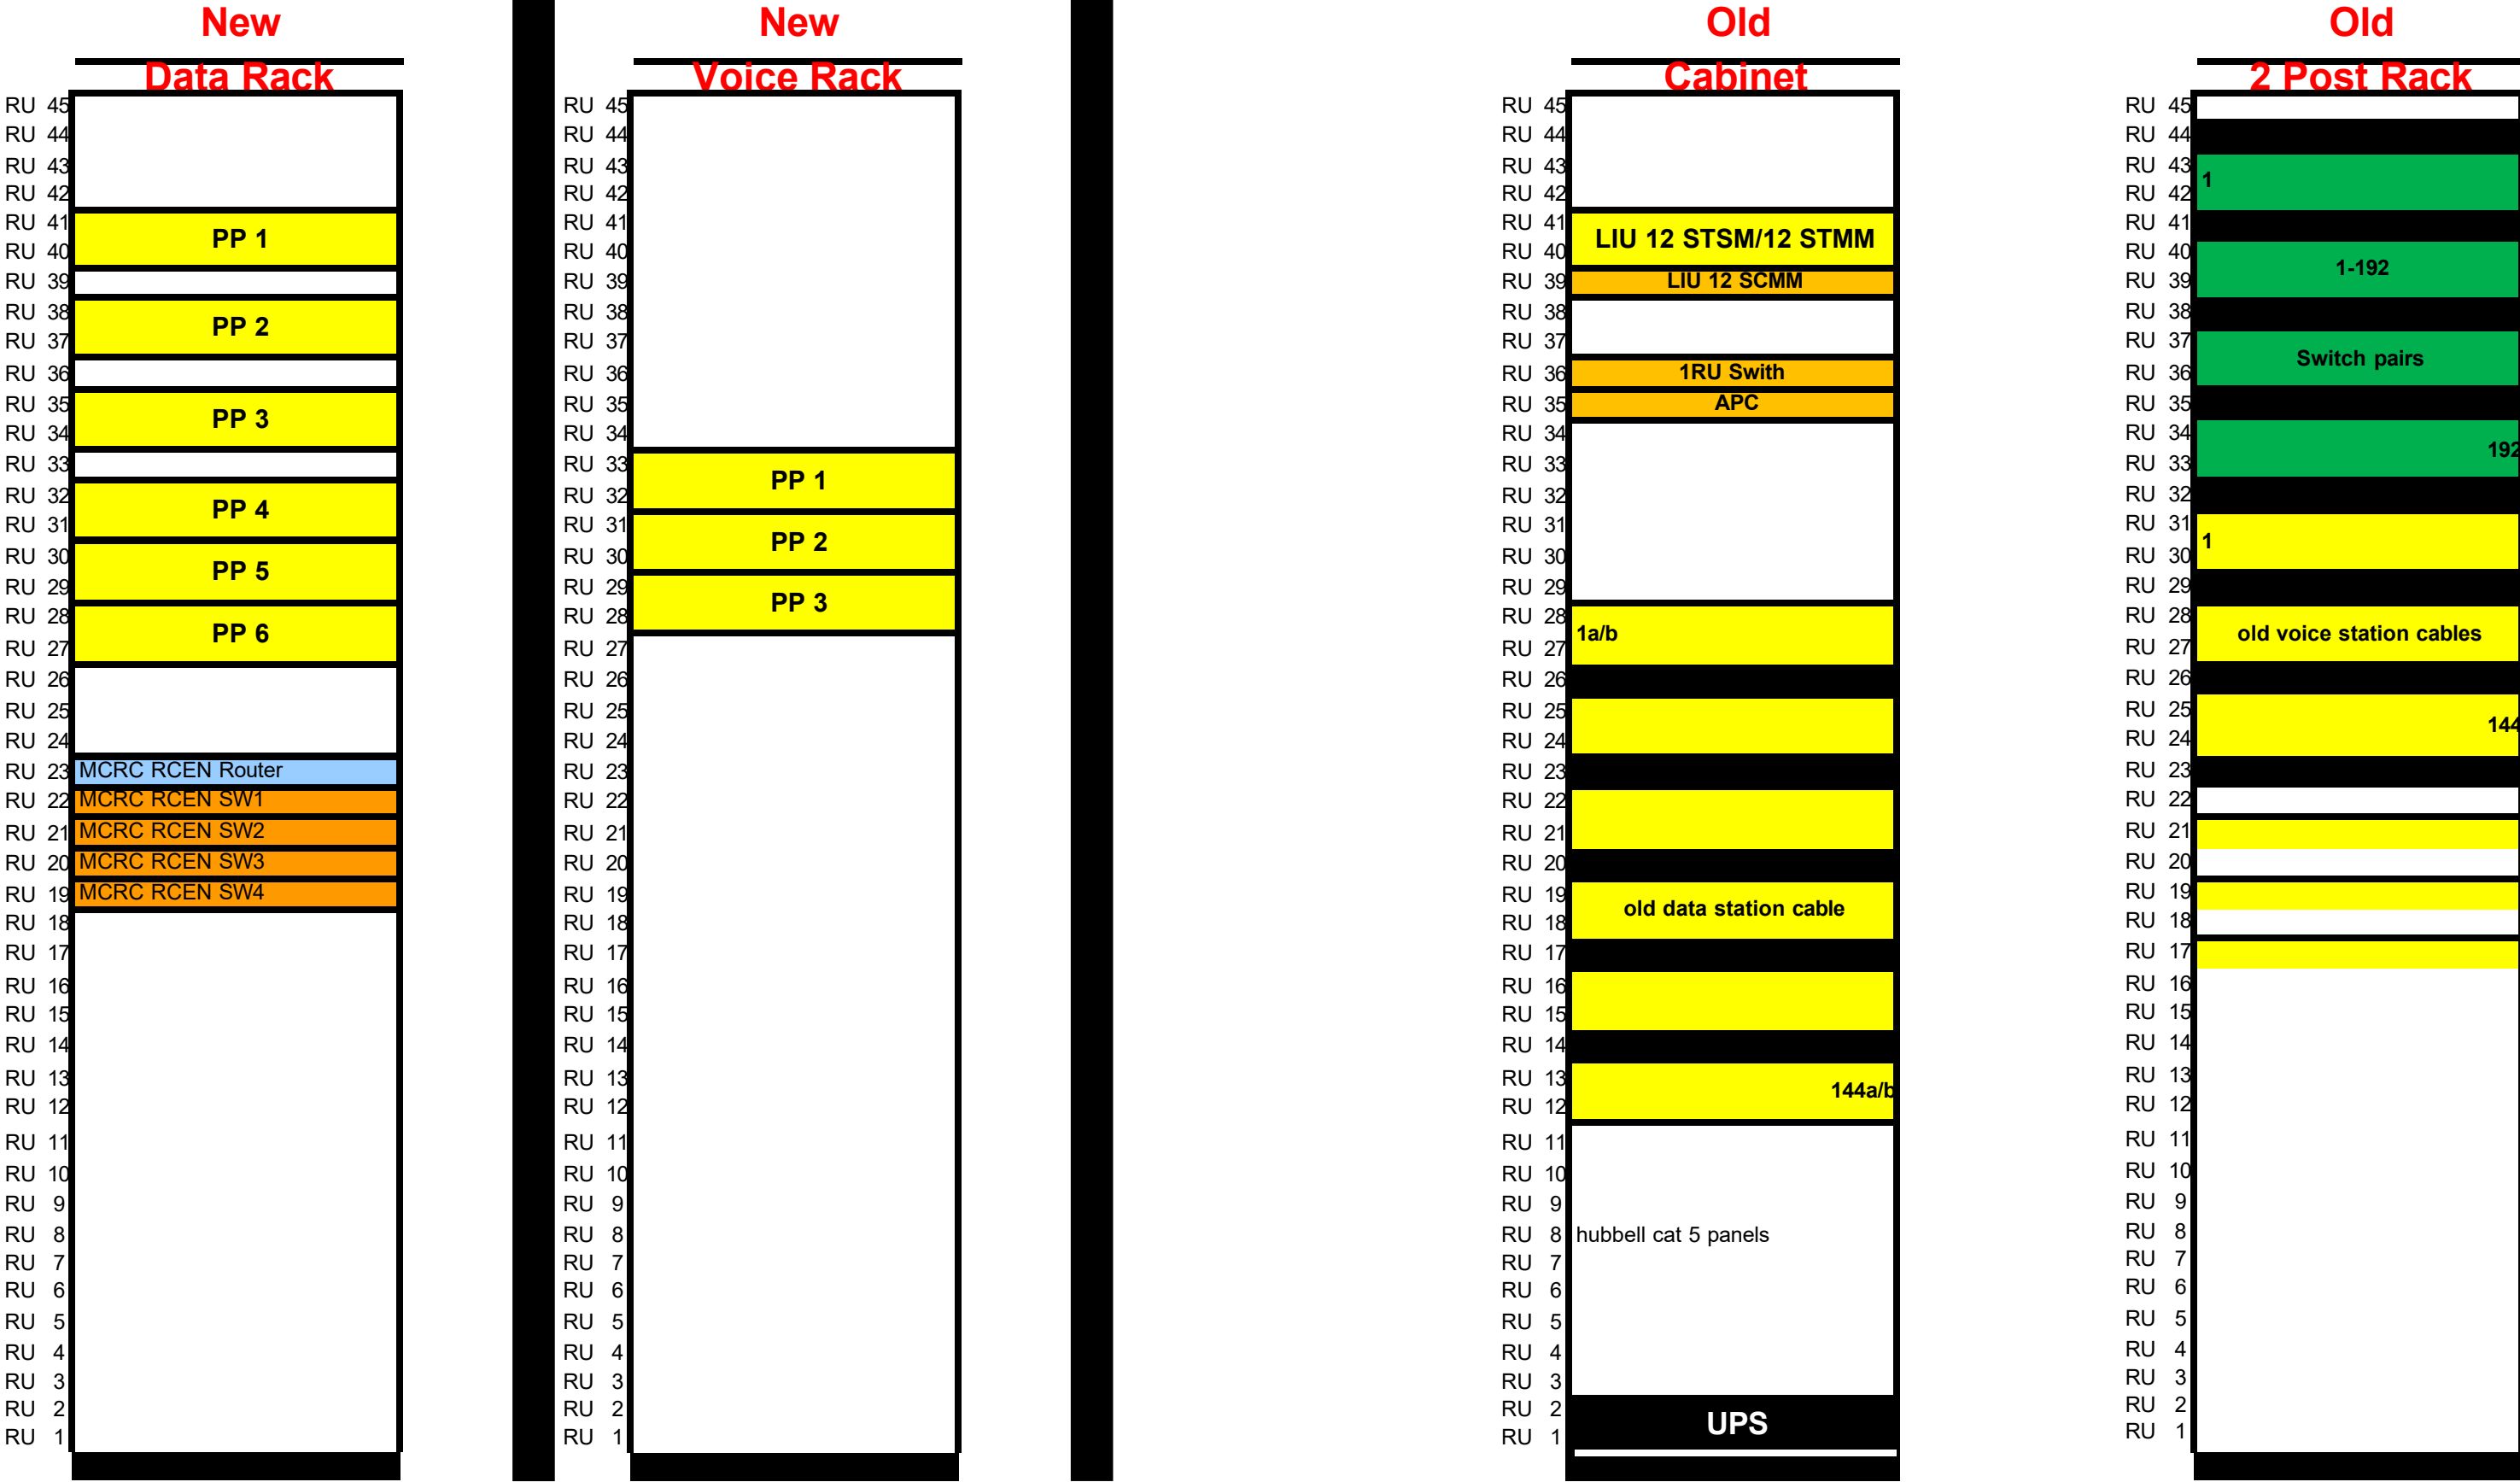

USMC Marsh Center - 2 East Telecom Room Patch Panel Reference

No Test	Passed	Failed	Marginal
---------	--------	--------	----------

1							6	7	2E-D 004A	2E-D 004B							12	13	2E-D 007A							18	19	2E-D 010A	2E-D 010B	2E-D 011A							24										
25							30	31	2E-D 016A							36	37							42	43	2E-D 022A							48														
Panel 1																																															
1							6	7							12	13							18	19							24																
25							30	31	2E-D 040A	2E-D 040B	2E-D 041A	2E-D 041B							36	37							42	43	2E-D 046A	2E-D 046B	2E-D 047A	2E-D 047B							48								
Panel 2																																															
1	2E-D 049A	2E-D 049B	2E-D 050A	2E-D 050B	2E-D 051A	2E-D 051B	6	7	2E-D 052A	2E-D 052B	2E-D 053A	2E-D 053B	2E-D 054A	2E-D 054B	12	13	2E-D 055A	2E-D 055B	2E-D 056A	2E-D 056B	2E-D 057A	2E-D 057B	18	19	2E-D 058A	2E-D 058B	2E-D 059A	2E-D 059B	2E-D 060A	2E-D 060B	24																
25	2E-D 061A	2E-D 061B	2E-D 062A	2E-D 062B	2E-D 063A	2E-D 063B	30	31	2E-D 064A	2E-D 064B	2E-D 065A	2E-D 065B	2E-D 066A	2E-D 066B	36	37	2E-D 067A	2E-D 067B	2E-D 068A	2E-D 068B	2E-D 069A	2E-D 069B	42	43	2E-D 070A	2E-D 070B	2E-D 071A	2E-D 071B	2E-D 072A	2E-D 072B	48																
Panel 3																																															
1	2E-D 073A	2E-D 073B	2E-D 074A	2E-D 074B	2E-D 075A	2E-D 075B	6	7	2E-D 076A	2E-D 076B	2E-D 077A	2E-D 077B	2E-D 078A	2E-D 078B	12	13	2E-D 079A	2E-D 079B	2E-D 080A	2E-D 080B	2E-D 081A	2E-D 081B	18	19	2E-D 082A	2E-D 082B	2E-D 083A	2E-D 083B	2E-D 084A	2E-D 084B	24																
25	2E-D 085A	2E-D 085B	2E-D 086A	2E-D 086B	2E-D 087A	2E-D 087B	30	31	2E-D 088A	2E-D 088B	2E-D 089A	2E-D 089B	2E-D 090A	2E-D 090B	36	37	2E-D 091A	2E-D 091B	2E-D 092A	2E-D 092B	2E-D 093A	2E-D 093B	42	43	2E-D 094A	2E-D 094B	2E-D 095A	2E-D 095B	2E-D 096A	2E-D 096B	48																
Panel 4																																															
1	2E-D 097A	2E-D 097B	2E-D 098A	2E-D 098B	2E-D 099A	2E-D 099B	6	7	2E-D 100A	2E-D 100B	2E-D 101A	2E-D 101B	2E-D 102A	2E-D 102B	12	13	2E-D 103A	2E-D 103B	2E-D 104A	2E-D 104B	2E-D 105A	2E-D 105B	18	19	2E-D 106A	2E-D 106B	2E-D 107A	2E-D 107B	2E-D 108A	2E-D 108B	24																
25	2E-D 109A	2E-D 109B	2E-D 110A	2E-D 110B	2E-D 111A	2E-D 111B	30	31	2E-D 112A	2E-D 112B	2E-D 113A	2E-D 113B	2E-D 114A	2E-D 114B	36	37	2E-D 115A	2E-D 115B	2E-D 116A	2E-D 116B	2E-D 117A	2E-D 117B	42	43	2E-D 118A	2E-D 118B	2E-D 119A	2E-D 119B	2E-D 120A	2E-D 120B	48																
Panel 5																																															
1	2E-D 121A	2E-D 121B	2E-D 122A	2E-D 122B	2E-D 123A	2E-D 123B	6	7	2E-D 124A	2E-D 124B	2E-D 125A	2E-D 125B	2E-D 126A	2E-D 126B	12	13	2E-D 127A	2E-D 127B	2E-D 128A	2E-D 128B	2E-D 129A	2E-D 129B	18	19	2E-D 130A	2E-D 130B	2E-D 131A	2E-D 131B	2E-D 132A	2E-D 132B	24																
25	2E-D 133A	2E-D 133B	2E-D 134A	2E-D 134B	2E-D 135A	2E-D 135B	30	31	2E-D 136A	2E-D 136B	2E-D 137A	2E-D 137B	2E-D 138A	2E-D 138B	36	37							42	43							48																
Panel 6																																															

Panel 1

Panel 2

Panel 3


Panel 4

Panel 5


Panel 6

276 Total
Data


249 Total
Data
Tested



139 Total
Voice

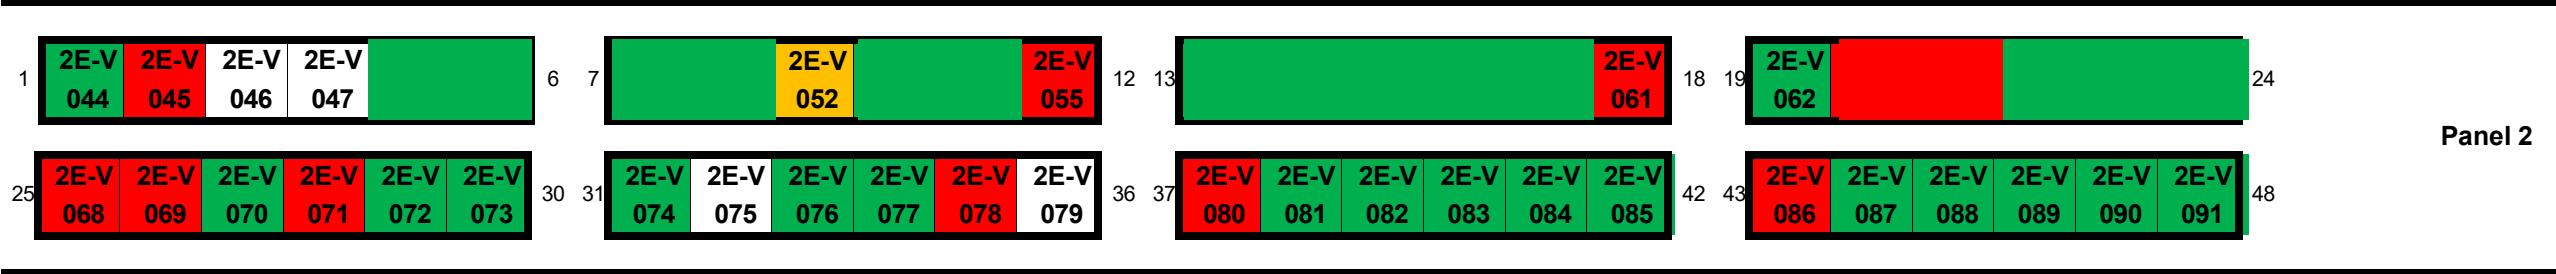

121 Total
Voice
Tested



East/South Side of Bldg

Outlet	Notes	Notes
2		
9	Biscuit off furniture	
10	Biscuit off furniture	
11	Biscuit off furniture	
12	Biscuit off furniture	A&B Data are swapped
16	Biscuit off furniture	
18	Biscuit off furniture	
20	Biscuit off furniture	
21	Biscuit off furniture	
22	Biscuit off furniture	
24	Biscuit off furniture	Voice Jack - something stuck in it
30	Biscuit off furniture	
33	Biscuit off furniture	
37	Biscuit off furniture	
42	Biscuit off furniture	
49	Biscuit off furniture	
50	Biscuit off furniture	
54	Biscuit off furniture	
55	Biscuit off furniture	
56	Biscuit off furniture	
58	Biscuit off furniture	
65		
76	Biscuit off furniture	
79	Biscuit off furniture	Voice Jack - something stuck in it
81	Biscuit off furniture	
82	Biscuit off furniture	
83	Biscuit off furniture	
84	Biscuit off furniture	
86	Biscuit off furniture	
111	Voice jack missing	
113	A Data jack missing	
114	Voice Jack missing	
115	No Faceplate	
116		A&B Data are swapped
134		
154		
156		

Failing Results Voice	Diagnosis	Possible Cause
1	Or/Wh, Wh/B, B/Wh open.	Bad patch panel port or termination
3	Wh/Or, Wh/Br open	Broken Jack/Pins/Termination
7	B/Wh open	Broken Jack/Pins/Termination
8	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
14	Gr/Wh, Wh/Br	Bad patch panel port or termination
18	Wh/Br open	Bad patch panel port or termination
25	Gr/Wh	Bad patch panel port or termination
32	Wh/Or open	Broken Jack/Pins/Termination. Possible cut cable
33	Return Loss - IDF Side	Poor termination
34	Return Loss - Both Sides	Poor termination
37	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
38	Wh/Or open	Broken Jack/Pins/Termination
39	Wh/Or open	Bad patch panel port or termination
43	Return Loss - Both Sides	Poor termination
45	Wh/Or, Or/Wh, Wh/Gr, Wh/Br open	Bad patch panel port or termination
55	Wh/Gr, Gr/Wh open	Bad patch panel port or termination
61	Wh/Or open	Bad patch panel port or termination
63	Wh/Or, Gr/Wh, Wh/Br	Broken Jack/Pins/Termination. Bad patch panel port or termination
64	Wh/Or open. Blue pair crossed	Broken Jack/Pins/Termination
68	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
69	Wh/Or open	Broken Jack/Pins/Termination
71	Or/Wh open	Broken Jack/Pins/Termination. Possible cut cable
78	Wh/Or open	Broken Jack/Pins/Termination
80	Wh/Or open	Broken Jack/Pins/Termination
86	Wh/Gr open	Broken Jack/Pins/Termination
97	Green & Brown Pairs Crossed	Poor Termination
110	Wh/Gr open	Broken Jack/Pins/Termination
Marginal Results-Voice	Diagnosis	Possible Cause
30	Return Loss - IDF Side	Poor Termination
36	Return Loss - IDF Side	Poor Termination
52	Cross Talk - WAO Side	Poor Termination
117	Cross Talk - WAO Side	Poor Termination
129	Cross Talk - WAO Side	Poor Termination

Failing Results Data	Diagnosis	Possible Cause
10B	Or/Wh, Wh/Gr open	Bad patch panel port or termination
11B	Wh/Gr, Wh/Br open	Bad patch panel port or termination
12A	Or/Wh open	Bad patch panel port or termination
12B	Wh/Br open	Bad patch panel port or termination
18A	Or/Wh, Wh/Or, Wh/Br open	Bad patch panel port or termination
20B	Or/Wh open	Bad patch panel port or termination
22A	Wh/Gr, Gr/Wh open	Broken Jack/Pins/Termination. Bad patch panel port or termination
24B	Wh/Or, B/Wh open	Broken Jack/Pins/Termination. Bad patch panel port or termination
27A	Or/Wh, Br/Wh open	Bad patch panel port or termination
27B	Or/Wh, Wh/Or, Gr/Wh open	Bad patch panel port or termination
33A	Gr/Wh Open	Bad patch panel port or termination
34A	Return Loss - Both Sides	Poor Termination
34B	Wh/Br open	Bad patch panel port or termination
35B	Wh/Or, Or/Wh, B/Wh open	Bad patch panel port or termination
36A	Or/Wh Open	Bad patch panel port or termination
36B	B/Wh open	Bad patch panel port or termination
44B	Wh/Br open	Bad patch panel port or termination
45B	Cross Talk - Both Sides	Poor Termination
65A	Wh/B open	Broken Jack/Pins/Termination
68B	B/Wh open	Bad patch panel port or termination
73B	Or/Wh open	Bad patch panel port or termination
79B	Cross Talk - WAO Side	Poor Termination
7A	Wh/Gr open	Broken Jack/Pins/Termination
80B	Cross Talk - WAO Side	Poor Termination
84B	Wh/Br open	Bad patch panel port or termination
85A	Wh/Or open	Bad patch panel port or termination
86A	Wh/Or open	Bad patch panel port or termination
91A	B/Wh open	Broken Jack/Pins/Termination
92A	Cross Talk - WAO Side	Poor Termination
94A	Cross Talk - WAO Side	Poor Termination
105A	Gr/Wh Open	Broken Jack/Pins/Termination
108B	Cross Talk - WAO Side	Poor Termination
111B	Gr/Wh Open	Broken Jack/Pins/Termination
117A	Wh/Or open	Broken Jack/Pins/Termination
119A	Cross Talk - WAO Side	Poor Termination
129A	Cross Talk - WAO Side	Poor Termination
134A	Or/Gr pairs reversed	Poor Termination
Marginal Results-Data	Diagnosis	Possible Cause
10A	Cross Talk - WAO Side	Poor Termination
16A	Return Loss - IDF Side	Poor Termination
21A	Cross Talk - WAO Side	Poor Termination
32A	Cross Talk - IDF Side	Poor Termination
41B	Return Loss - IDF Side	Poor Termination
95A	Cross Talk - WAO Side	Poor Termination
112A	Cross Talk - IDF Side	Poor Termination

North/West Telecom Room

New	
Data Rack	
RU 45	
RU 44	
RU 43	
RU 42	
RU 41	PP 1
RU 40	
RU 39	
RU 38	PP 1
RU 37	
RU 36	
RU 35	PP 1
RU 34	
RU 33	
RU 32	PP 1
RU 31	
RU 30	
RU 29	PP 1
RU 28	
RU 27	
RU 26	PP 1
RU 25	
RU 24	
RU 23	PP 1
RU 22	
RU 21	
RU 20	
RU 19	
RU 18	
RU 17	
RU 16	1RU Switch
RU 15	1RU Switch
RU 14	1RU Switch
RU 13	1RU Switch
RU 12	1RU Switch
RU 11	1RU Switch
RU 10	1RU Switch
RU 9	1RU Switch
RU 8	UPS
RU 7	
RU 6	UPS
RU 5	
RU 4	UPS
RU 3	
RU 2	UPS
RU 1	

New	
Voice Rack	
RU 45	
RU 44	
RU 43	
RU 42	
RU 41	
RU 40	
RU 39	
RU 38	
RU 37	
RU 36	
RU 35	
RU 34	
RU 33	
RU 32	PP 1
RU 31	
RU 30	
RU 29	PP 1
RU 28	
RU 27	
RU 26	PP 1
RU 25	
RU 24	
RU 23	PP 1
RU 22	
RU 21	
RU 20	
RU 19	
RU 18	
RU 17	
RU 16	1RU Switch
RU 15	
RU 14	
RU 13	
RU 12	
RU 11	
RU 10	
RU 9	
RU 8	
RU 7	
RU 6	
RU 5	
RU 4	
RU 3	
RU 2	
RU 1	

Old	
Cabinet	
RU 45	
RU 44	
RU 43	
RU 42	
RU 41	LIU 12 STSM/12 STMM
RU 40	
RU 39	LIU 12 SCMM
RU 38	
RU 37	
RU 36	
RU 35	
RU 34	
RU 33	
RU 32	
RU 31	
RU 30	
RU 29	
RU 28	
RU 27	
RU 26	
RU 25	1a/b
RU 24	
RU 23	
RU 22	
RU 21	
RU 20	
RU 19	
RU 18	
RU 17	
RU 16	
RU 15	
RU 14	
RU 13	
RU 12	
RU 11	
RU 10	
RU 9	
RU 8	
RU 7	159 a/b
RU 6	
RU 5	
RU 4	
RU 3	
RU 2	
RU 1	

Old	
2 Post Rack	
RU 45	
RU 44	
RU 43	
RU 42	1
RU 41	
RU 40	1-192
RU 39	
RU 38	
RU 37	Switch pairs
RU 36	
RU 35	
RU 34	192
RU 33	
RU 32	
RU 31	1
RU 30	
RU 29	
RU 28	old voice station cables
RU 27	
RU 26	
RU 25	
RU 24	
RU 23	
RU 22	
RU 21	159
RU 20	
RU 19	
RU 18	
RU 17	
RU 16	
RU 15	
RU 14	
RU 13	
RU 12	
RU 11	
RU 10	
RU 9	
RU 8	
RU 7	
RU 6	
RU 5	
RU 4	
RU 3	
RU 2	
RU 1	


USMC Marsh Center - 2 West Telecom Room Patch Panel Reference																								No Test	Passed	Failed	Marginal				
1	2W-D 001A	2W-D 001B	2W-D 002A	2W-D 002B	2W-D 003A	2W-D 003B	6	7	2W-D 004A	2W-D 004B	2W-D 005A	2W-D 005B	2W-D 006A	2W-D 006B	12	13	2W-D 007A	2W-D 007B	2W-D 008A	2W-D 008B	2W-D 009A	2W-D 009B	18	19	2W-D 010A	2W-D 010B	2W-D 011A	2W-D 011B	2W-D 012A	2W-D 012B	24
25	2W-D 013A	2W-D 013B					30	31					36	37					42	43					2W-D 024A	2W-D 024B			48		
1	2W-D 025A	2W-D 025B	2W-D 026A	2W-D 026B	2W-D 027A	2W-D 027B	6	7					12	13			2W-D 032A	2W-D 032B	2W-D 033A	2W-D 033B	18	19	2W-D 034A	2W-D 034B	2W-D 035A	2W-D 035B	2W-D 036A	2W-D 036B	24		
25	2W-D 037A	2W-D 037B					30	31					36	37					42	43			2W-D 042A	2W-D 042B	48	49			54		
1	2W-D 049A	2W-D 049B	2W-D 050A	2W-D 050B	2W-D 051A	2W-D 051B	6	7	2W-D 052A	2W-D 052B	2W-D 053A	2W-D 053B	2W-D 054A	2W-D 054B	12	13	2W-D 055A	2W-D 055B	2W-D 056A	2W-D 056B	2W-D 057A	2W-D 057B	18	19	2W-D 058A	2W-D 058B	2W-D 059A	2W-D 059B	2W-D 060A	2W-D 060B	24
25	2W-D 061A	2W-D 061B	2W-D 062A	2W-D 062B	2W-D 063A	2W-D 063B	30	31	2W-D 064A	2W-D 064B	2W-D 065A	2W-D 065B	2W-D 066A	2W-D 066B	36	37	2W-D 067A	2W-D 067B	2W-D 068A	2W-D 068B	2W-D 069A	2W-D 069B	42	43	2W-D 070A	2W-D 070B	2W-D 071A	2W-D 071B	2W-D 072A	2W-D 072B	48
1	2W-D 073A	2W-D 073B	2W-D 074A	2W-D 074B	2W-D 075A	2W-D 075B	6	7	2W-D 076A	2W-D 076B	2W-D 077A	2W-D 077B	2W-D 078A	2W-D 078B	12	13	2W-D 079A	2W-D 079B	2W-D 080A	2W-D 080B	2W-D 081A	2W-D 081B	18	19	2W-D 082A	2W-D 082B	2W-D 083A	2W-D 083B	2W-D 084A	2W-D 084B	24
25	2W-D 085A	2W-D 085B	2W-D 086A	2W-D 086B	2W-D 087A	2W-D 087B	30	31	2W-D 088A	2W-D 088B	2W-D 089A	2W-D 089B	2W-D 090A	2W-D 090B	36	37	2W-D 091A	2W-D 091B	2W-D 092A	2W-D 092B	2W-D 093A	2W-D 093B	42	43	2W-D 094A	2W-D 094B	2W-D 095A	2W-D 095B	2W-D 096A	2W-D 096B	48
1	2W-D 097A	2W-D 097B	2W-D 098A	2W-D 098B	2W-D 099A	2W-D 099B	6	7	2W-D 100A	2W-D 100B	2W-D 101A	2W-D 101B	2W-D 102A	2W-D 102B	12	13	2W-D 103A	2W-D 103B	2W-D 104A	2W-D 104B	2W-D 105A	2W-D 105B	18	19	2W-D 106A	2W-D 106B	2W-D 107A	2W-D 107B	2W-D 108A	2W-D 108B	24
25	2W-D 109A	2W-D 109B	2W-D 110A	2W-D 110B	2W-D 111A	2W-D 111B	30	31	2W-D 112A	2W-D 112B	2W-D 113A	2W-D 113B	2W-D 114A	2W-D 114B	36	37	2W-D 115A	2W-D 115B	2W-D 116A	2W-D 116B	2W-D 117A	2W-D 117B	42	43	2W-D 118A	2W-D 118B	2W-D 119A	2W-D 119B	2W-D 120A	2W-D 120B	48
1	2W-D 121A	2W-D 121B	2W-D 122A	2W-D 122B	2W-D 123A	2W-D 123B	6	7	2W-D 124A	2W-D 124B	2W-D 125A	2W-D 125B	2W-D 126A	2W-D 126B	12	13	2W-D 127A	2W-D 127B	2W-D 128A	2W-D 128B	2W-D 129A	2W-D 129B	18	19	2W-D 130A	2W-D 130B	2W-D 131A	2W-D 131B	2W-D 132A	2W-D 132B	24
25	2W-D 133A	2W-D 133B	2W-D 134A	2W-D 134B	2W-D 135A	2W-D 135B	30	31	2W-D 136A	2W-D 136B	2W-D 137A	2W-D 137B	2W-D 138A	2W-D 138B	36	37	2W-D 139A	2W-D 139B	2W-D 140A	2W-D 140B	2W-D 141A	2W-D 141B	42	43	2W-D 142A	2W-D 142B	2W-D 143A	2W-D 143B	2W-D 144A	2W-D 144B	48
1	2W-D 145A	2W-D 145B	2W-D 146A	2W-D 146B	2W-D 147A	2W-D 147B	24	24	2W-D 148A	2W-D 148B	2W-D 149A	2W-D 149B	2W-D 150A	2W-D 150B	24	24	2W-D 151A	2W-D 151B	2W-D 152A	2W-D 152B	2W-D 153A	2W-D 153B	24	24	2W-D 154A	2W-D 154B	2W-D 155A	2W-D 155B	2W-D 156A	2W-D 156B	48

312 Total Data

279 Total Data Tested

312 Total
Data

279 Total
Data
Tested

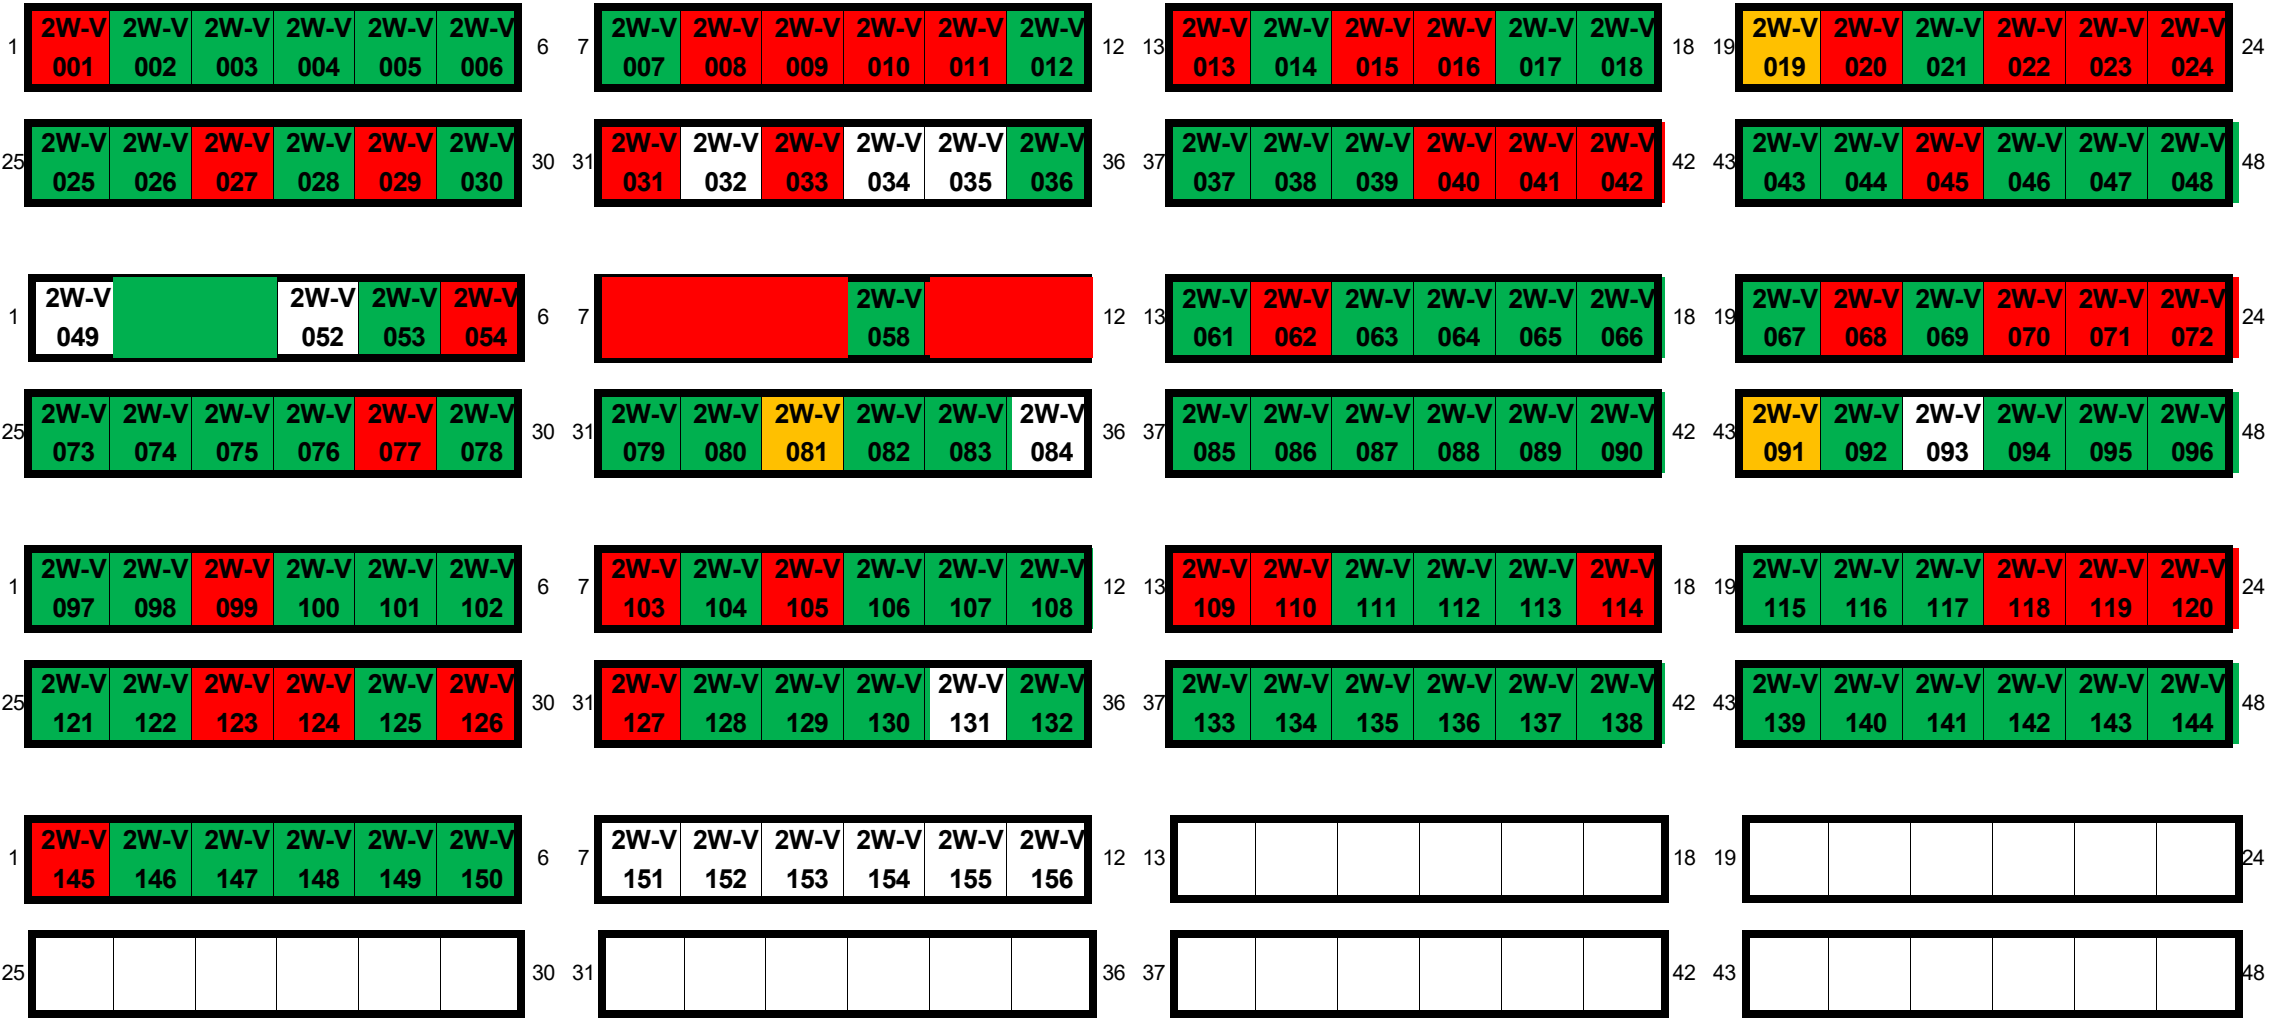

Panel 1

Panel 2

Panel 3

Panel 3

156 Total
Voice

142 Total
Voice
Tested

West/North Side of Bldg

Outlet	Notes	Notes
1	A&B are reversed	
9	Biscuit not mounted	
10	Biscuit not mounted	
12	Biscuit not mounted	B Data Missing
13	Biscuit not mounted	
17	Biscuit not mounted	
19	Biscuit not mounted	
21	Biscuit not mounted	
23	Biscuit not mounted	
24		Data Cables Missing
29	Biscuit not mounted	
33	Biscuit not mounted	Data Cables Missing
43	Biscuit not mounted	
44	Biscuit not mounted	
45	Biscuit not mounted	Jack loose
46	Biscuit not mounted	
54		Jacks loose
58	No biscuit, no label	
59	Biscuit not mounted	
61	Biscuit not mounted	
64	B data is a white jack	
65	A&B are reversed	
66	A&B are reversed	
67	A&B are reversed	B Cable is missing
68	A&B are reversed	
69	A & B are reversed	
70	A & B are reversed	
71	Voice and B Data are reversed	
72	A & B are reversed	
78	Not Labeled	
86	Not Labeled	
96		Behind Furniture
99	Biscuit not mounted	
100	Biscuit not mounted	
101	Biscuit not mounted	
103	Biscuit not mounted	
104	Biscuit not mounted	
106	Biscuit not mounted	Jacks loose
107	Biscuit not mounted	Jacks loose
109	Biscuit not mounted	
111	Cables are cut	Voice cables missing
111	A&B are reversed	Jacks loose
115		
116		
117	Biscuit not mounted	
119	No biscuit	B Jack Broken
120	Biscuit not mounted	
125	Biscuit not mounted	
126	Biscuit not mounted	
132	No biscuit, no label	
133	No biscuit, no label	
135		
139	Biscuit not mounted	
140		Jacks loose
141	Biscuit not mounted	
142	Biscuit not mounted	

143	Biscuit not mounted	
148	Broken Biscuit	Behind Furniture

Failing Results Voice	Diagnosis	Possible Cause
1	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
8	Return Loss - Both ends	Poor Termination
9	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
10	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
11	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
13	Wh/Or, Or/Wh, Br/Wh open. Or/Wh, Wh/Gr Shorted	Broken Jack/Pins/Termination. Poor termination at patch panel
15	Wh/Or open	Broken Jack/Pins/Termination
16	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
20	Wh/Or open	Broken Jack/Pins/Termination
22	Wh/Or open	Broken Jack/Pins/Termination
23	Wh/Or, Wh/Gr, Br/Wh open	Broken Jack/Pins/Termination. Bad patch panel port or termination
24	Wh/Or, Or/Wh open	Broken Jack/Pins/Termination. Bad patch panel port or termination
27	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
29	Br/Wh open	Broken Jack/Pins/Termination
31	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
33	Or/Gr pairs reversed	Poor Termination
40	Cross Talk - WAO Side	Poor Termination
41	Wh/Or open	Broken Jack/Pins/Termination
42	Wh/Br open	Bad patch panel port or termination
45	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
54	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
55	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
56	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
57	Gr/Br pairs reversed	Poor Termination
59	Wh/B, B/Wh, Wh/Gr, Gr/Wh open	Broken Jack/Pins/Termination
60	Gr/Wh open	Broken Jack/Pins/Termination
62	Wh/Or open	Broken Jack/Pins/Termination
68	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
70	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
71	Br/Wh open	Broken Jack/Pins/Termination
72	Wh/Or open	Broken Jack/Pins/Termination
77	Cross Talk - WAO Side	Poor Termination
99	Wh/Or open	Broken Jack/Pins/Termination
103	Wh/Or open	Broken Jack/Pins/Termination
105	Wh/Or open	Broken Jack/Pins/Termination
109	Wh/Or open	Broken Jack/Pins/Termination
110	Cross Talk - WAO Side	Poor Termination
114	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
118	Wh/Or open	Broken Jack/Pins/Termination
119	Wh/Gr open	Broken Jack/Pins/Termination
120	Wh/B open	Broken Jack/Pins/Termination
123	Wh/Or open	Broken Jack/Pins/Termination
124	Wh/Or open	Broken Jack/Pins/Termination
126	Wh/Or, Br/Wh open	Broken Jack/Pins/Termination
127	Wh/Or open	Broken Jack/Pins/Termination
145	Br/Wh open	Broken Jack/Pins/Termination
Marginal Results-Voice	Diagnosis	Possible Cause
19	Cross Talk - WAO Side	Poor Termination
81	Cross Talk - WAO Side	Poor Termination
91	Cross Talk - WAO Side	Poor Termination

Failing Results Data	Diagnosis	Possible Cause
1A	Gr/Wh open	Broken Jack/Pins/Termination
5B	Cross Talk - WAO Side	Poor Termination
9A	B/Wh, Wh/Br open	Broken Jack/Pins/Termination
25B	Wh/B, B/Wh open	Bad patch panel port or termination
26B	Br/Wh open	Bad patch panel port or termination
27B	Green Pair Open at jack, Shorted at Patch Panel	Broken Jack/Pins/Termination. Bad patch panel port or termination
36A	Wh/Gr open	Broken Jack/Pins/Termination
37B	Or/Wh open	Bad patch panel port or termination
42A	Cross Talk - WAO Side	Poor Termination
45A	Cross Talk - WAO Side	Poor Termination
47B	Cross Talk - WAO Side	Poor Termination
51B	Gr/Wh open	Bad patch panel port or termination
53A	Wh/Or open	Bad patch panel port or termination
54B	Gr/Wh open	Bad patch panel port or termination
57A	Wh/B open, Green Pair crossed	Broken Jack/Pins/Termination
57B	Wh/B, B/Wh, Wh/Or open. Green Pair Crossed	Broken Jack/Pins/Termination
58A	Wh/Gr, Gr/Wh open	Broken Jack/Pins/Termination
58B	Wh/Or, Or/Wh open	Bad patch panel port or termination
59A	Wh/B, Wh/Gr open	Broken Jack/Pins/Termination
59B	Wh/B, Gr/Wh open	Broken Jack/Pins/Termination
62B	Wh/Gr, Gr/Wh open. Brown Pair Crossed	Broken Jack/Pins/Termination
67A	Blue and Brown Pairs Shorted	Poor Termination
68A	Cross Talk - WAO Side	Poor Termination
68B	Wh/Or, Or/Wh, Wh/Gr, Gr/Wh open	Bad patch panel port or termination
69B	Gr/Wh open	Bad patch panel port or termination
72B	Or/Wh, Wh/Gr open	Bad patch panel port or termination
73A	Wh/Or open	Bad patch panel port or termination
73B	Or/Wh open	Bad patch panel port or termination
76B	Wh/Gr open	Broken Jack/Pins/Termination
78A	Cross Talk - WAO Side	Poor Termination
82B	Wh/B open	Broken Jack/Pins/Termination
97B	Wh/Gr open	Bad patch panel port or termination
98B	Or/Wh open	Bad patch panel port or termination
100A	Wh/B, B/Wh open	Broken Jack/Pins/Termination
106B	Wh/B, Wh/Gr open	Broken Jack/Pins/Termination
110B	Cross Talk - WAO Side	Poor Termination
118A	Cross Talk - TR Side	Poor Termination
120B	B/Wh, Wh/Gr open	Broken Jack/Pins/Termination
122A	Cross Talk - WAO Side	Poor Termination
Marginal Results-Data	Diagnosis	Possible Cause
13B	Return Loss - IDF Side	Poor Termination
80B	Cross Talk - IDF Side	Poor Termination

Telecom Room Notes

East

Temperature at center of room - 5' AFF

78.4 degrees Fahrenheit

Dimensions

10'11" x 9'11"

(2) 2-post racks with new Voice/Data Patch Panels

Neither rack is bolted down

Neither rack is bonded to ground

Newly installed ladder rack is not bonded to ground

Overhead cable tray does not support the new cable (blue)

Excessive slack hanging behind the patch panels on both racks

Cables are not labeled behind the panels with machine printed labels

Neither rack has sufficient vertical management for
station cabling - rear, or patch cabling - front

UPS devices are sitting on the floor. Power cables are loose across the floor.

Telecom door is not secure

All existing white cable enters the room from floor trough.

(1) existing enclosed cabinet housing old data panels and
fiber optic LIUs

(1) APC device and (1) 1ru switch.

This switch may be the connectivity for wireless access points

(1) existing/old 2-post rack.

This rack contains patch panels with single pair connectivity - most like old telephone switch ties

This rack also contains old voice station cable patch panels.

There are excessively long patch cables between the switch tie panel and the new voice panels
No cable management or support for these cables.

There is a considerable amount of trash/debris/abandoned equipment on the floor.

Telecom Room Recommendations.

Perform a phone switch audit to determine if there are any active analog lines still in use.

If there are no active switch ports, recommend removing all patch cables and the old rack and panels

Cut all old white cable back to the floor trough/entry to the telecom room if feasible

Determine where the wireless access point cables are terminated and migrate them to the new 2-post data

Migrate Fiber Optic LIUs from the enclosed cabinet to the new 2-post rack if there is sufficient slack in the

Migrate active equipment from the enclosed cabinet to the new 2-post rack.

Remove all old data cabling from the cabinet and cut back to the floor trough/entry to the telecom room if

Remove the old cabinet and 2-post rack from the room.

Add cable tray over top the new 2-post data rack to properly support the cable slack.

Redress/support all blue cabling - new voice and data.

Telecom Room Notes

West

Temperature at center of room - 5' AFF

78 degrees Fahrenheit

Dimensions

9'0" x 10'0"

(2) 2-post racks with new Voice/Data Patch Panels

Overhead cable tray does not support the new cable (blue)

Excessive slack hanging behind the patch panels on both racks

Cables are not labeled behind the panels with machine printed labels

Neither rack has sufficient vertical management for
station cabling - rear, or patch cabling - front

UPS devices are sitting on the floor. Power cables are loose across the floor.

Telecom door is not secure

All existing white cable enters the room from floor trough.

(1) existing enclosed cabinet housing old data panels and
fiber optic LIUs

(1) existing/old 2-post rack.

This rack contains patch panels with single pair connectivity - most like old telephone switch ties

This rack also contains old voice station cable patch panels.

There are excessively long patch cables between the switch tie panel and the new voice panels

No cable management or support for these cables.

There is a considerable amount of trash/debris/abandoned equipment on the floor.

Telecom Room Recommendations.

Perform a phone switch audit to determine if there are any active analog lines still in use.

If there are no active switch ports, recommend removing all patch cables and the old rack and panels

Cut all old white cable back to the floor trough/entry to the telecom room if feasible

Determine where the wireless access point cable are terminated and migrate them to the new 2-post data rack.

Migrate Fiber Optic LIUs from the enclosed cabinet to the new 2-post rack if there is sufficient slack in the cable.

Migrate active equipment from the enclosed cabinet to the new 2-post rack.

Remove all old data cabling from the cabinet and cut back to the floor trough/entry to the telecom room if feasible

Remove the old cabinet and 2-post rack from the room.

Add cable tray over top the new 2-post data rack to properly support the cable slack.

Redress/support all blue cabling - new voice and data.

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2E-D-001A	PASS	TIA Cat 6 Perm. Link	236 ft	2.0 dB (NEXT)	07/07/2026 10:58 AM
2E-D-001B	PASS	TIA Cat 6 Perm. Link	236 ft	4.5 dB (NEXT)	07/07/2026 10:59 AM
2E-D-002A	PASS	TIA Cat 6 Perm. Link	231 ft	4.2 dB (NEXT)	07/07/2026 10:38 AM
2E-D-002B	PASS	TIA Cat 6 Perm. Link	231 ft	3.7 dB (NEXT)	07/07/2026 10:38 AM
2E-D-003A	PASS	TIA Cat 6 Perm. Link	219 ft	8.2 dB (NEXT)	07/07/2026 02:48 PM
2E-D-003B	PASS	TIA Cat 6 Perm. Link	219 ft	2.3 dB (NEXT)	07/07/2026 02:49 PM
2E-D-005A	PASS	TIA Cat 6 Perm. Link	224 ft	4.0 dB (NEXT)	07/07/2026 10:43 AM
2E-D-005B	PASS	TIA Cat 6 Perm. Link	224 ft	6.6 dB (NEXT)	07/07/2026 10:45 AM
2E-D-006A	PASS	TIA Cat 6 Perm. Link	231 ft	7.8 dB (NEXT)	07/07/2026 10:47 AM
2E-D-006B	PASS	TIA Cat 6 Perm. Link	231 ft	2.4 dB (NEXT)	07/07/2026 10:48 AM
2E-D-007A	FAIL	TIA Cat 6 Perm. Link	236 ft	N/A	07/07/2026 10:49 AM
2E-D-007B	PASS	TIA Cat 6 Perm. Link	236 ft	7.7 dB (NEXT)	07/07/2026 10:51 AM
2E-D-008A	PASS	TIA Cat 6 Perm. Link	207 ft	4.1 dB (NEXT)	07/07/2026 02:55 PM
2E-D-008B	PASS	TIA Cat 6 Perm. Link	208 ft	7.1 dB (NEXT)	07/07/2026 02:56 PM
2E-D-009A	PASS	TIA Cat 6 Perm. Link	204 ft	7.2 dB (NEXT)	07/07/2026 02:11 PM
2E-D-009B	PASS	TIA Cat 6 Perm. Link	204 ft	5.0 dB (NEXT)	07/07/2026 02:11 PM
2E-D-010A	PASS*	TIA Cat 6 Perm. Link	204 ft	1.0 dB (NEXT)	07/07/2026 02:13 PM
2E-D-010B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 02:15 PM
2E-D-011A	PASS	TIA Cat 6 Perm. Link	198 ft	3.8 dB (NEXT)	07/07/2026 02:20 PM
2E-D-011B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 02:22 PM
2E-D-012A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 02:02 PM
2E-D-012B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 02:03 PM
2E-D-013A	PASS	TIA Cat 6 Perm. Link	210 ft	1.7 dB (NEXT)	07/07/2026 11:01 AM
2E-D-013B	PASS	TIA Cat 6 Perm. Link	211 ft	5.2 dB (NEXT)	07/07/2026 11:02 AM
2E-D-014A	PASS	TIA Cat 6 Perm. Link	214 ft	4.9 dB (NEXT)	07/07/2026 10:39 AM
2E-D-014B	PASS	TIA Cat 6 Perm. Link	214 ft	6.2 dB (NEXT)	07/07/2026 10:40 AM
2E-D-015A	PASS	TIA Cat 6 Perm. Link	204 ft	4.8 dB (NEXT)	07/07/2026 02:36 PM
2E-D-015B	PASS	TIA Cat 6 Perm. Link	204 ft	5.9 dB (NEXT)	07/07/2026 02:37 PM
2E-D-016A	PASS*	TIA Cat 6 Perm. Link	199 ft	1.1 dB (NEXT)	07/07/2026 02:29 PM
2E-D-016B	PASS	TIA Cat 6 Perm. Link	200 ft	3.9 dB (NEXT)	07/07/2026 02:30 PM
2E-D-017A	PASS	TIA Cat 6 Perm. Link	204 ft	4.4 dB (NEXT)	07/07/2026 02:32 PM
2E-D-017B	PASS	TIA Cat 6 Perm. Link	204 ft	2.0 dB (NEXT)	07/07/2026 02:33 PM
2E-D-018A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 01:48 PM
2E-D-018B	PASS	TIA Cat 6 Perm. Link	199 ft	6.6 dB (NEXT)	07/07/2026 01:48 PM
2E-D-019A	PASS	TIA Cat 6 Perm. Link	204 ft	6.1 dB (NEXT)	07/07/2026 01:55 PM
2E-D-019B	PASS	TIA Cat 6 Perm. Link	205 ft	6.3 dB (NEXT)	07/07/2026 01:56 PM
2E-D-020A	PASS	TIA Cat 6 Perm. Link	194 ft	2.9 dB (NEXT)	07/07/2026 01:50 PM
2E-D-020B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 01:52 PM
2E-D-021A	PASS*	TIA Cat 6 Perm. Link	187 ft	0.4 dB (NEXT)	07/07/2026 01:44 PM
2E-D-021B	PASS	TIA Cat 6 Perm. Link	188 ft	2.0 dB (NEXT)	07/07/2026 01:45 PM
2E-D-022A	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/07/2026 02:26 PM
2E-D-022B	PASS	TIA Cat 6 Perm. Link	187 ft	4.2 dB (NEXT)	07/07/2026 02:27 PM
2E-D-023A	PASS	TIA Cat 6 Perm. Link	193 ft	2.8 dB (NEXT)	07/07/2026 02:05 PM
2E-D-023B	PASS	TIA Cat 6 Perm. Link	192 ft	7.8 dB (NEXT)	07/07/2026 02:06 PM
2E-D-024A	PASS	TIA Cat 6 Perm. Link	189 ft	3.5 dB (NEXT)	07/07/2026 02:17 PM
2E-D-024B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 02:18 PM
2E-D-025A	PASS	TIA Cat 6 Perm. Link	196 ft	4.6 dB (NEXT)	07/07/2026 02:08 PM
2E-D-025B	PASS	TIA Cat 6 Perm. Link	196 ft	4.1 dB (NEXT)	07/07/2026 02:09 PM
2E-D-026A	PASS	TIA Cat 6 Perm. Link	196 ft	3.3 dB (NEXT)	07/07/2026 01:32 PM
2E-D-026B	PASS	TIA Cat 6 Perm. Link	196 ft	5.6 dB (NEXT)	07/07/2026 01:33 PM
2E-D-027A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 01:36 PM
2E-D-027B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 01:38 PM
2E-D-028A	PASS	TIA Cat 6 Perm. Link	194 ft	5.7 dB (NEXT)	07/07/2026 01:20 PM
2E-D-028B	PASS	TIA Cat 6 Perm. Link	194 ft	7.2 dB (NEXT)	07/07/2026 01:21 PM
2E-D-029A	PASS	TIA Cat 6 Perm. Link	187 ft	4.6 dB (NEXT)	07/07/2026 01:17 PM
2E-D-029B	PASS	TIA Cat 6 Perm. Link	187 ft	4.3 dB (NEXT)	07/07/2026 01:17 PM
2E-D-030A	PASS	TIA Cat 6 Perm. Link	168 ft	2.0 dB (NEXT)	07/07/2026 01:40 PM
2E-D-030B	PASS	TIA Cat 6 Perm. Link	167 ft	4.0 dB (NEXT)	07/07/2026 01:41 PM
2E-D-031A	PASS	TIA Cat 6 Perm. Link	174 ft	5.3 dB (NEXT)	07/07/2026 01:23 PM
2E-D-031B	PASS	TIA Cat 6 Perm. Link	174 ft	8.7 dB (NEXT)	07/07/2026 01:23 PM
2E-D-032A	PASS*	TIA Cat 6 Perm. Link	180 ft	0.3 dB (NEXT)	07/07/2026 01:26 PM
2E-D-032B	PASS	TIA Cat 6 Perm. Link	179 ft	6.9 dB (NEXT)	07/07/2026 01:27 PM
2E-D-033A	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/07/2026 01:29 PM
2E-D-033B	PASS	TIA Cat 6 Perm. Link	185 ft	2.7 dB (NEXT)	07/07/2026 01:30 PM
2E-D-034A	FAIL	TIA Cat 6 Perm. Link	176 ft	3.1 dB (NEXT)	07/07/2026 12:41 PM
2E-D-034B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 12:42 PM
2E-D-035A	PASS	TIA Cat 6 Perm. Link	169 ft	5.0 dB (NEXT)	07/07/2026 12:44 PM
2E-D-035B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 12:45 PM
2E-D-036A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 12:50 PM
2E-D-036B	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/07/2026 12:50 PM
2E-D-037A	PASS	TIA Cat 6 Perm. Link	162 ft	3.0 dB (NEXT)	07/07/2026 12:47 PM
2E-D-037B	PASS	TIA Cat 6 Perm. Link	161 ft	6.6 dB (NEXT)	07/07/2026 12:47 PM
2E-D-038A	PASS	TIA Cat 6 Perm. Link	149 ft	6.9 dB (NEXT)	07/07/2026 12:37 PM
2E-D-038B	PASS	TIA Cat 6 Perm. Link	149 ft	3.7 dB (NEXT)	07/07/2026 12:37 PM
2E-D-039A	PASS	TIA Cat 6 Perm. Link	157 ft	6.5 dB (NEXT)	07/08/2026 09:48 AM
2E-D-039B	PASS	TIA Cat 6 Perm. Link	157 ft	6.5 dB (NEXT)	07/08/2026 09:49 AM
2E-D-041A	PASS	TIA Cat 6 Perm. Link	190 ft	3.9 dB (NEXT)	07/07/2026 01:13 PM
2E-D-041B	PASS*	TIA Cat 6 Perm. Link	191 ft	3.9 dB (NEXT)	07/07/2026 01:15 PM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2E-D-042A	PASS	TIA Cat 6 Perm. Link	187 ft	4.5 dB (NEXT)	07/07/2026 01:10 PM
2E-D-042B	PASS	TIA Cat 6 Perm. Link	187 ft	3.9 dB (NEXT)	07/07/2026 01:11 PM
2E-D-043A	PASS	TIA Cat 6 Perm. Link	162 ft	5.8 dB (NEXT)	07/07/2026 02:58 PM
2E-D-043B	PASS	TIA Cat 6 Perm. Link	161 ft	1.9 dB (NEXT)	07/07/2026 02:59 PM
2E-D-044A	PASS	TIA Cat 6 Perm. Link	146 ft	5.9 dB (NEXT)	07/07/2026 10:05 AM
2E-D-044B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 10:06 AM
2E-D-045A	PASS	TIA Cat 6 Perm. Link	137 ft	1.1 dB (NEXT)	07/07/2026 09:58 AM
2E-D-045B	FAIL	TIA Cat 6 Perm. Link	1 ft	-1.3 dB (NEXT)	07/07/2026 10:00 AM
2E-D-048A	PASS	TIA Cat 6 Perm. Link	169 ft	3.2 dB (NEXT)	07/07/2026 12:33 PM
2E-D-048B	PASS	TIA Cat 6 Perm. Link	169 ft	5.7 dB (NEXT)	07/07/2026 12:33 PM
2E-D-049A	PASS	TIA Cat 6 Perm. Link	172 ft	3.3 dB (NEXT)	07/07/2026 12:29 PM
2E-D-049B	PASS	TIA Cat 6 Perm. Link	172 ft	7.6 dB (NEXT)	07/07/2026 12:30 PM
2E-D-050A	PASS	TIA Cat 6 Perm. Link	151 ft	3.0 dB (NEXT)	07/07/2026 12:26 PM
2E-D-050B	PASS	TIA Cat 6 Perm. Link	151 ft	4.5 dB (NEXT)	07/07/2026 12:27 PM
2E-D-051A	PASS	TIA Cat 6 Perm. Link	157 ft	6.0 dB (NEXT)	07/07/2026 12:24 PM
2E-D-051B	PASS	TIA Cat 6 Perm. Link	157 ft	5.8 dB (NEXT)	07/07/2026 12:25 PM
2E-D-052A	PASS	TIA Cat 6 Perm. Link	157 ft	5.9 dB (NEXT)	07/07/2026 12:21 PM
2E-D-052B	PASS	TIA Cat 6 Perm. Link	158 ft	7.9 dB (NEXT)	07/07/2026 12:22 PM
2E-D-053A	PASS	TIA Cat 6 Perm. Link	165 ft	4.8 dB (NEXT)	07/07/2026 12:52 PM
2E-D-053B	PASS	TIA Cat 6 Perm. Link	165 ft	7.9 dB (NEXT)	07/07/2026 12:53 PM
2E-D-054A	PASS	TIA Cat 6 Perm. Link	173 ft	5.3 dB (NEXT)	07/07/2026 12:55 PM
2E-D-054B	PASS	TIA Cat 6 Perm. Link	173 ft	3.6 dB (NEXT)	07/07/2026 12:56 PM
2E-D-055A	PASS	TIA Cat 6 Perm. Link	172 ft	4.1 dB (NEXT)	07/07/2026 12:57 PM
2E-D-055B	PASS	TIA Cat 6 Perm. Link	172 ft	4.4 dB (NEXT)	07/07/2026 12:58 PM
2E-D-056A	PASS	TIA Cat 6 Perm. Link	152 ft	2.6 dB (NEXT)	07/07/2026 01:00 PM
2E-D-056B	PASS	TIA Cat 6 Perm. Link	152 ft	6.9 dB (NEXT)	07/07/2026 01:00 PM
2E-D-057A	PASS	TIA Cat 6 Perm. Link	158 ft	6.7 dB (NEXT)	07/07/2026 01:03 PM
2E-D-057B	PASS	TIA Cat 6 Perm. Link	158 ft	7.5 dB (NEXT)	07/07/2026 01:03 PM
2E-D-058A	PASS	TIA Cat 6 Perm. Link	159 ft	5.8 dB (NEXT)	07/07/2026 01:06 PM
2E-D-058B	PASS	TIA Cat 6 Perm. Link	159 ft	3.7 dB (NEXT)	07/07/2026 01:07 PM
2E-D-059A	PASS	TIA Cat 6 Perm. Link	144 ft	7.1 dB (NEXT)	07/07/2026 09:49 AM
2E-D-059B	PASS	TIA Cat 6 Perm. Link	147 ft	4.9 dB (NEXT)	07/07/2026 09:50 AM
2E-D-060A	PASS	TIA Cat 6 Perm. Link	139 ft	4.5 dB (NEXT)	07/07/2026 09:52 AM
2E-D-060B	PASS	TIA Cat 6 Perm. Link	139 ft	8.2 dB (NEXT)	07/07/2026 09:53 AM
2E-D-061A	PASS	TIA Cat 6 Perm. Link	135 ft	7.0 dB (NEXT)	07/07/2026 09:55 AM
2E-D-061B	PASS	TIA Cat 6 Perm. Link	133 ft	1.2 dB (NEXT)	07/07/2026 09:56 AM
2E-D-062A	PASS	TIA Cat 6 Perm. Link	139 ft	4.3 dB (NEXT)	07/07/2026 09:45 AM
2E-D-062B	PASS	TIA Cat 6 Perm. Link	138 ft	5.0 dB (NEXT)	07/07/2026 09:46 AM
2E-D-063A	PASS	TIA Cat 6 Perm. Link	132 ft	5.7 dB (NEXT)	07/07/2026 09:41 AM
2E-D-063B	PASS	TIA Cat 6 Perm. Link	130 ft	3.2 dB (NEXT)	07/07/2026 09:42 AM
2E-D-064A	PASS	TIA Cat 6 Perm. Link	125 ft	3.2 dB (NEXT)	07/07/2026 09:38 AM
2E-D-064B	PASS	TIA Cat 6 Perm. Link	125 ft	6.9 dB (NEXT)	07/07/2026 09:39 AM
2E-D-065A	FAIL	TIA Cat 6 Perm. Link	124 ft	N/A	07/07/2026 09:33 AM
2E-D-065B	PASS	TIA Cat 6 Perm. Link	124 ft	2.9 dB (NEXT)	07/07/2026 09:34 AM
2E-D-066A	PASS	TIA Cat 6 Perm. Link	131 ft	6.3 dB (NEXT)	07/07/2026 09:29 AM
2E-D-066B	PASS	TIA Cat 6 Perm. Link	130 ft	6.2 dB (NEXT)	07/07/2026 09:30 AM
2E-D-067A	PASS	TIA Cat 6 Perm. Link	138 ft	6.4 dB (NEXT)	07/07/2026 09:26 AM
2E-D-067B	PASS	TIA Cat 6 Perm. Link	138 ft	4.5 dB (NEXT)	07/07/2026 09:27 AM
2E-D-068A	PASS	TIA Cat 6 Perm. Link	118 ft	6.3 dB (NEXT)	07/07/2026 09:22 AM
2E-D-068B	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/07/2026 09:23 AM
2E-D-069A	PASS	TIA Cat 6 Perm. Link	112 ft	5.5 dB (NEXT)	07/07/2026 09:20 AM
2E-D-069B	PASS	TIA Cat 6 Perm. Link	112 ft	3.7 dB (NEXT)	07/07/2026 09:20 AM
2E-D-070A	PASS	TIA Cat 6 Perm. Link	104 ft	7.2 dB (NEXT)	07/07/2026 09:17 AM
2E-D-070B	PASS	TIA Cat 6 Perm. Link	105 ft	6.3 dB (NEXT)	07/07/2026 09:18 AM
2E-D-071A	PASS	TIA Cat 6 Perm. Link	113 ft	5.3 dB (NEXT)	07/07/2026 09:12 AM
2E-D-071B	PASS	TIA Cat 6 Perm. Link	114 ft	4.1 dB (NEXT)	07/07/2026 09:12 AM
2E-D-072A	PASS	TIA Cat 6 Perm. Link	123 ft	2.7 dB (NEXT)	07/07/2026 09:09 AM
2E-D-072B	PASS	TIA Cat 6 Perm. Link	123 ft	4.0 dB (NEXT)	07/07/2026 09:09 AM
2E-D-073A	PASS	TIA Cat 6 Perm. Link	105 ft	6.5 dB (NEXT)	07/07/2026 08:59 AM
2E-D-073B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 09:00 AM
2E-D-074A	PASS	TIA Cat 6 Perm. Link	107 ft	8.6 dB (NEXT)	07/07/2026 08:56 AM
2E-D-074B	PASS	TIA Cat 6 Perm. Link	107 ft	5.6 dB (NEXT)	07/07/2026 08:57 AM
2E-D-076A	PASS	TIA Cat 6 Perm. Link	113 ft	6.6 dB (NEXT)	07/07/2026 12:13 PM
2E-D-076B	PASS	TIA Cat 6 Perm. Link	112 ft	7.2 dB (NEXT)	07/07/2026 12:15 PM
2E-D-077A	PASS	TIA Cat 6 Perm. Link	109 ft	6.8 dB (NEXT)	07/07/2026 12:10 PM
2E-D-077B	PASS	TIA Cat 6 Perm. Link	103 ft	4.9 dB (NEXT)	07/07/2026 12:11 PM
2E-D-078A	PASS	TIA Cat 6 Perm. Link	100 ft	4.9 dB (NEXT)	07/07/2026 12:07 PM
2E-D-078B	PASS	TIA Cat 6 Perm. Link	102 ft	6.5 dB (NEXT)	07/07/2026 12:07 PM
2E-D-079A	PASS	TIA Cat 6 Perm. Link	94 ft	5.7 dB (NEXT)	07/07/2026 10:25 AM
2E-D-079B	FAIL	TIA Cat 6 Perm. Link	92 ft	-3.0 dB (NEXT)	07/07/2026 10:27 AM
2E-D-080A	PASS	TIA Cat 6 Perm. Link	104 ft	6.6 dB (NEXT)	07/07/2026 12:16 PM
2E-D-080B	FAIL	TIA Cat 6 Perm. Link	103 ft	-0.6 dB (NEXT)	07/07/2026 12:18 PM
2E-D-081A	PASS	TIA Cat 6 Perm. Link	76 ft	4.0 dB (NEXT)	07/07/2026 08:26 AM
2E-D-081B	PASS	TIA Cat 6 Perm. Link	76 ft	1.1 dB (NEXT)	07/07/2026 08:29 AM
2E-D-082A	PASS	TIA Cat 6 Perm. Link	88 ft	5.8 dB (NEXT)	07/07/2026 08:32 AM
2E-D-082B	PASS	TIA Cat 6 Perm. Link	89 ft	5.7 dB (NEXT)	07/07/2026 08:34 AM
2E-D-083A	PASS	TIA Cat 6 Perm. Link	94 ft	3.5 dB (NEXT)	07/07/2026 08:36 AM
2E-D-083B	PASS	TIA Cat 6 Perm. Link	95 ft	2.6 dB (NEXT)	07/07/2026 08:36 AM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2E-D-084A	PASS	TIA Cat 6 Perm. Link	90 ft	5.6 dB (NEXT)	07/07/2026 08:40 AM
2E-D-084B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 08:41 AM
2E-D-085A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 08:45 AM
2E-D-085B	PASS	TIA Cat 6 Perm. Link	83 ft	5.0 dB (NEXT)	07/07/2026 08:45 AM
2E-D-086A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 08:48 AM
2E-D-086B	PASS	TIA Cat 6 Perm. Link	76 ft	7.6 dB (NEXT)	07/07/2026 08:50 AM
2E-D-087A	PASS	TIA Cat 6 Perm. Link	142 ft	7.4 dB (NEXT)	07/09/2026 10:46 AM
2E-D-087B	PASS	TIA Cat 6 Perm. Link	142 ft	4.9 dB (NEXT)	07/09/2026 10:47 AM
2E-D-088A	PASS	TIA Cat 6 Perm. Link	142 ft	4.3 dB (NEXT)	07/09/2026 10:34 AM
2E-D-088B	PASS	TIA Cat 6 Perm. Link	143 ft	6.1 dB (NEXT)	07/09/2026 10:35 AM
2E-D-089A	PASS	TIA Cat 6 Perm. Link	142 ft	6.2 dB (NEXT)	07/09/2026 10:35 AM
2E-D-089B	PASS	TIA Cat 6 Perm. Link	142 ft	6.9 dB (NEXT)	07/09/2026 10:35 AM
2E-D-090A	PASS	TIA Cat 6 Perm. Link	142 ft	5.8 dB (NEXT)	07/09/2026 10:40 AM
2E-D-090B	PASS	TIA Cat 6 Perm. Link	142 ft	5.1 dB (NEXT)	07/09/2026 10:41 AM
2E-D-091A	FAIL	TIA Cat 6 Perm. Link	126 ft	N/A	07/09/2026 10:29 AM
2E-D-091B	PASS	TIA Cat 6 Perm. Link	126 ft	6.9 dB (NEXT)	07/09/2026 10:29 AM
2E-D-092A	FAIL	TIA Cat 6 Perm. Link	125 ft	-1.8 dB (NEXT)	07/09/2026 10:30 AM
2E-D-092B	PASS	TIA Cat 6 Perm. Link	126 ft	5.4 dB (NEXT)	07/09/2026 10:31 AM
2E-D-093A	PASS	TIA Cat 6 Perm. Link	127 ft	1.6 dB (NEXT)	07/09/2026 10:31 AM
2E-D-093B	PASS	TIA Cat 6 Perm. Link	127 ft	7.6 dB (NEXT)	07/09/2026 10:31 AM
2E-D-094A	FAIL	TIA Cat 6 Perm. Link	127 ft	-0.9 dB (NEXT)	07/09/2026 10:32 AM
2E-D-094B	PASS	TIA Cat 6 Perm. Link	129 ft	3.2 dB (NEXT)	07/09/2026 10:32 AM
2E-D-095A	PASS*	TIA Cat 6 Perm. Link	128 ft	0.8 dB (NEXT)	07/09/2026 10:33 AM
2E-D-095B	PASS	TIA Cat 6 Perm. Link	127 ft	2.3 dB (NEXT)	07/09/2026 10:33 AM
2E-D-096A	PASS	TIA Cat 6 Perm. Link	127 ft	6.0 dB (NEXT)	07/09/2026 10:33 AM
2E-D-096B	PASS	TIA Cat 6 Perm. Link	128 ft	7.0 dB (NEXT)	07/09/2026 10:34 AM
2E-D-097A	PASS	TIA Cat 6 Perm. Link	113 ft	7.7 dB (NEXT)	07/09/2026 10:27 AM
2E-D-097B	PASS	TIA Cat 6 Perm. Link	114 ft	6.7 dB (NEXT)	07/09/2026 10:27 AM
2E-D-098A	PASS	TIA Cat 6 Perm. Link	114 ft	7.8 dB (NEXT)	07/09/2026 10:22 AM
2E-D-098B	PASS	TIA Cat 6 Perm. Link	114 ft	8.4 dB (NEXT)	07/09/2026 10:22 AM
2E-D-099A	PASS	TIA Cat 6 Perm. Link	114 ft	1.9 dB (NEXT)	07/09/2026 10:24 AM
2E-D-099B	PASS	TIA Cat 6 Perm. Link	113 ft	6.4 dB (NEXT)	07/09/2026 10:24 AM
2E-D-100A	PASS	TIA Cat 6 Perm. Link	112 ft	7.1 dB (NEXT)	07/09/2026 10:25 AM
2E-D-100B	PASS	TIA Cat 6 Perm. Link	112 ft	6.2 dB (NEXT)	07/09/2026 10:25 AM
2E-D-101A	PASS	TIA Cat 6 Perm. Link	112 ft	7.1 dB (NEXT)	07/09/2026 10:25 AM
2E-D-101B	PASS	TIA Cat 6 Perm. Link	113 ft	5.5 dB (NEXT)	07/09/2026 10:26 AM
2E-D-102A	PASS	TIA Cat 6 Perm. Link	112 ft	3.5 dB (NEXT)	07/09/2026 10:26 AM
2E-D-102B	PASS	TIA Cat 6 Perm. Link	112 ft	5.5 dB (NEXT)	07/09/2026 10:26 AM
2E-D-103A	PASS	TIA Cat 6 Perm. Link	126 ft	8.4 dB (NEXT)	07/09/2026 11:02 AM
2E-D-103B	PASS	TIA Cat 6 Perm. Link	127 ft	5.9 dB (NEXT)	07/09/2026 11:03 AM
2E-D-104A	PASS	TIA Cat 6 Perm. Link	155 ft	5.9 dB (NEXT)	07/09/2026 10:58 AM
2E-D-104B	PASS	TIA Cat 6 Perm. Link	154 ft	5.6 dB (NEXT)	07/09/2026 10:58 AM
2E-D-105A	FAIL	TIA Cat 6 Perm. Link	154 ft	N/A	07/09/2026 10:53 AM
2E-D-105B	PASS	TIA Cat 6 Perm. Link	155 ft	5.2 dB (NEXT)	07/09/2026 10:55 AM
2E-D-106A	PASS	TIA Cat 6 Perm. Link	154 ft	6.1 dB (NEXT)	07/09/2026 10:55 AM
2E-D-106B	PASS	TIA Cat 6 Perm. Link	154 ft	4.9 dB (NEXT)	07/09/2026 10:54 AM
2E-D-107A	PASS	TIA Cat 6 Perm. Link	155 ft	2.9 dB (NEXT)	07/09/2026 10:55 AM
2E-D-107B	PASS	TIA Cat 6 Perm. Link	153 ft	7.9 dB (NEXT)	07/09/2026 10:56 AM
2E-D-108A	PASS	TIA Cat 6 Perm. Link	154 ft	4.0 dB (NEXT)	07/09/2026 10:56 AM
2E-D-108B	FAIL	TIA Cat 6 Perm. Link	154 ft	-0.5 dB (NEXT)	07/09/2026 10:56 AM
2E-D-109A	PASS	TIA Cat 6 Perm. Link	154 ft	4.4 dB (NEXT)	07/09/2026 10:57 AM
2E-D-109B	PASS	TIA Cat 6 Perm. Link	154 ft	7.3 dB (NEXT)	07/09/2026 10:57 AM
2E-D-110A	PASS	TIA Cat 6 Perm. Link	140 ft	5.8 dB (NEXT)	07/09/2026 10:49 AM
2E-D-110B	PASS	TIA Cat 6 Perm. Link	140 ft	2.4 dB (NEXT)	07/09/2026 10:49 AM
2E-D-111A	PASS	TIA Cat 6 Perm. Link	142 ft	5.7 dB (NEXT)	07/09/2026 10:50 AM
2E-D-111B	FAIL	TIA Cat 6 Perm. Link	141 ft	N/A	07/09/2026 10:51 AM
2E-D-112A	PASS*	TIA Cat 6 Perm. Link	132 ft	0.6 dB (NEXT)	07/10/2026 07:25 AM
2E-D-112B	PASS	TIA Cat 6 Perm. Link	132 ft	7.2 dB (NEXT)	07/10/2026 07:25 AM
2E-D-113B	PASS	TIA Cat 6 Perm. Link	133 ft	5.5 dB (NEXT)	07/10/2026 07:23 AM
2E-D-114A	PASS	TIA Cat 6 Perm. Link	132 ft	4.7 dB (NEXT)	07/10/2026 07:15 AM
2E-D-114B	PASS	TIA Cat 6 Perm. Link	132 ft	2.7 dB (NEXT)	07/10/2026 07:15 AM
2E-D-115A	PASS	TIA Cat 6 Perm. Link	154 ft	4.2 dB (NEXT)	07/10/2026 07:12 AM
2E-D-115B	PASS	TIA Cat 6 Perm. Link	152 ft	5.1 dB (NEXT)	07/10/2026 07:13 AM
2E-D-116A	PASS	TIA Cat 6 Perm. Link	150 ft	4.1 dB (NEXT)	07/10/2026 07:08 AM
2E-D-116B	PASS	TIA Cat 6 Perm. Link	152 ft	1.4 dB (NEXT)	07/10/2026 07:09 AM
2E-D-117A	FAIL	TIA Cat 6 Perm. Link	152 ft	N/A	07/10/2026 07:06 AM
2E-D-117B	PASS	TIA Cat 6 Perm. Link	152 ft	5.5 dB (NEXT)	07/10/2026 07:06 AM
2E-D-118A	PASS	TIA Cat 6 Perm. Link	152 ft	2.7 dB (NEXT)	07/10/2026 07:05 AM
2E-D-118B	PASS	TIA Cat 6 Perm. Link	153 ft	5.2 dB (NEXT)	07/10/2026 07:04 AM
2E-D-119A	FAIL	TIA Cat 6 Perm. Link	160 ft	-3.5 dB (NEXT)	07/08/2026 06:25 AM
2E-D-119B	PASS	TIA Cat 6 Perm. Link	159 ft	7.6 dB (NEXT)	07/08/2026 06:26 AM
2E-D-120A	PASS	TIA Cat 6 Perm. Link	166 ft	5.3 dB (NEXT)	07/08/2026 06:46 AM
2E-D-120B	PASS	TIA Cat 6 Perm. Link	165 ft	4.7 dB (NEXT)	07/08/2026 06:47 AM
2E-D-121A	PASS	TIA Cat 6 Perm. Link	165 ft	3.9 dB (NEXT)	07/08/2026 09:55 AM
2E-D-121B	PASS	TIA Cat 6 Perm. Link	165 ft	6.3 dB (NEXT)	07/08/2026 09:56 AM
2E-D-123A	PASS	TIA Cat 6 Perm. Link	120 ft	2.3 dB (NEXT)	07/10/2026 05:59 AM
2E-D-123B	PASS	TIA Cat 6 Perm. Link	119 ft	6.8 dB (NEXT)	07/10/2026 05:59 AM
2E-D-124A	PASS	TIA Cat 6 Perm. Link	120 ft	5.9 dB (NEXT)	07/10/2026 06:05 AM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2E-D-124B	PASS	TIA Cat 6 Perm. Link	120 ft	4.6 dB (NEXT)	07/10/2026 06:06 AM
2E-D-125A	PASS	TIA Cat 6 Perm. Link	98 ft	2.3 dB (NEXT)	07/10/2026 07:30 AM
2E-D-125B	PASS	TIA Cat 6 Perm. Link	98 ft	2.3 dB (NEXT)	07/10/2026 07:31 AM
2E-D-126A	PASS	TIA Cat 6 Perm. Link	96 ft	3.5 dB (NEXT)	07/10/2026 07:29 AM
2E-D-126B	PASS	TIA Cat 6 Perm. Link	96 ft	5.3 dB (NEXT)	07/10/2026 07:29 AM
2E-D-127A	PASS	TIA Cat 6 Perm. Link	89 ft	3.6 dB (NEXT)	07/10/2026 06:58 AM
2E-D-127B	PASS	TIA Cat 6 Perm. Link	90 ft	3.3 dB (NEXT)	07/10/2026 06:58 AM
2E-D-128A	PASS	TIA Cat 6 Perm. Link	85 ft	5.4 dB (NEXT)	07/10/2026 07:00 AM
2E-D-128B	PASS	TIA Cat 6 Perm. Link	85 ft	2.5 dB (NEXT)	07/10/2026 07:00 AM
2E-D-129A	FAIL	TIA Cat 6 Perm. Link	39 ft	-0.6 dB (NEXT)	07/10/2026 07:40 AM
2E-D-129B	PASS	TIA Cat 6 Perm. Link	40 ft	4.5 dB (NEXT)	07/10/2026 07:38 AM
2E-D-130A	PASS	TIA Cat 6 Perm. Link	43 ft	4.0 dB (NEXT)	07/10/2026 07:41 AM
2E-D-130B	PASS	TIA Cat 6 Perm. Link	43 ft	1.7 dB (NEXT)	07/10/2026 07:41 AM
2E-D-134A	FAIL	TIA Cat 6 Perm. Link	84 ft	N/A	07/07/2026 09:07 AM
2E-D-134B	PASS	TIA Cat 6 Perm. Link	84 ft	2.6 dB (NEXT)	07/07/2026 09:07 AM

Total Length:	33612 ft
Number of Reports:	249
Number of Passing Reports:	212
Number of Failing Reports:	37
Number of Warning Reports:	0
Documentation Only:	0

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2E-V-001	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 10:58 AM
2E-V-002	PASS	TIA Cat 6 Perm. Link	231 ft	5.8 dB (NEXT)	07/07/2026 10:24 AM
2E-V-003	FAIL	TIA Cat 6 Perm. Link	218 ft	N/A	07/07/2026 03:48 PM
2E-V-005	PASS	TIA Cat 6 Perm. Link	224 ft	1.4 dB (NEXT)	07/07/2026 10:43 AM
2E-V-006	PASS	TIA Cat 6 Perm. Link	231 ft	4.5 dB (NEXT)	07/07/2026 10:47 AM
2E-V-007	FAIL	TIA Cat 6 Perm. Link	237 ft	N/A	07/07/2026 10:50 AM
2E-V-008	FAIL	TIA Cat 6 Perm. Link	209 ft	N/A	07/07/2026 03:55 PM
2E-V-009	PASS	TIA Cat 6 Perm. Link	206 ft	6.1 dB (NEXT)	07/07/2026 03:10 PM
2E-V-010	PASS	TIA Cat 6 Perm. Link	204 ft	5.8 dB (NEXT)	07/07/2026 03:13 PM
2E-V-011	PASS	TIA Cat 6 Perm. Link	199 ft	5.0 dB (NEXT)	07/07/2026 03:16 PM
2E-V-012	PASS	TIA Cat 6 Perm. Link	193 ft	3.8 dB (NEXT)	07/07/2026 02:58 PM
2E-V-013	PASS	TIA Cat 6 Perm. Link	211 ft	5.2 dB (NEXT)	07/07/2026 11:01 AM
2E-V-014	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 10:41 AM
2E-V-015	PASS	TIA Cat 6 Perm. Link	204 ft	5.5 dB (NEXT)	07/07/2026 03:36 PM
2E-V-016	PASS	TIA Cat 6 Perm. Link	200 ft	6.4 dB (NEXT)	07/07/2026 03:29 PM
2E-V-017	PASS	TIA Cat 6 Perm. Link	204 ft	5.9 dB (NEXT)	07/07/2026 03:32 PM
2E-V-018	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 02:47 PM
2E-V-019	PASS	TIA Cat 6 Perm. Link	206 ft	6.3 dB (NEXT)	07/07/2026 02:55 PM
2E-V-020	PASS	TIA Cat 6 Perm. Link	196 ft	1.8 dB (NEXT)	07/07/2026 02:50 PM
2E-V-021	PASS	TIA Cat 6 Perm. Link	189 ft	5.5 dB (NEXT)	07/07/2026 02:43 PM
2E-V-022	PASS	TIA Cat 6 Perm. Link	187 ft	8.9 dB (NEXT)	07/07/2026 03:24 PM
2E-V-023	PASS	TIA Cat 6 Perm. Link	194 ft	7.8 dB (NEXT)	07/07/2026 03:05 PM
2E-V-025	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/07/2026 03:08 PM
2E-V-026	PASS	TIA Cat 6 Perm. Link	195 ft	9.1 dB (NEXT)	07/07/2026 02:32 PM
2E-V-027	PASS	TIA Cat 6 Perm. Link	189 ft	6.4 dB (NEXT)	07/07/2026 02:35 PM
2E-V-028	PASS	TIA Cat 6 Perm. Link	194 ft	6.1 dB (NEXT)	07/07/2026 02:19 PM
2E-V-029	PASS	TIA Cat 6 Perm. Link	187 ft	6.4 dB (NEXT)	07/07/2026 02:17 PM
2E-V-030	PASS*	TIA Cat 6 Perm. Link	169 ft	4.9 dB (NEXT)	07/07/2026 02:40 PM
2E-V-031	PASS	TIA Cat 6 Perm. Link	174 ft	4.0 dB (NEXT)	07/07/2026 02:23 PM
2E-V-032	FAIL	TIA Cat 6 Perm. Link	181 ft	N/A	07/07/2026 02:26 PM
2E-V-033	FAIL	TIA Cat 6 Perm. Link	187 ft	6.3 dB (NEXT)	07/07/2026 02:29 PM
2E-V-034	FAIL	TIA Cat 6 Perm. Link	177 ft	1.5 dB (NEXT)	07/07/2026 01:40 PM
2E-V-035	PASS	TIA Cat 6 Perm. Link	169 ft	5.7 dB (NEXT)	07/07/2026 01:44 PM
2E-V-036	PASS*	TIA Cat 6 Perm. Link	154 ft	4.6 dB (NEXT)	07/07/2026 01:49 PM
2E-V-037	FAIL	TIA Cat 6 Perm. Link	161 ft	N/A	07/07/2026 01:47 PM
2E-V-038	FAIL	TIA Cat 6 Perm. Link	149 ft	N/A	07/07/2026 01:36 PM
2E-V-039	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/08/2026 10:48 AM
2E-V-041	PASS	TIA Cat 6 Perm. Link	191 ft	7.6 dB (NEXT)	07/07/2026 02:13 PM
2E-V-042	PASS	TIA Cat 6 Perm. Link	188 ft	4.9 dB (NEXT)	07/07/2026 02:11 PM
2E-V-043	FAIL	TIA Cat 6 Perm. Link	165 ft	0.0 dB (NEXT)	07/07/2026 03:58 PM
2E-V-044	PASS	TIA Cat 6 Perm. Link	147 ft	7.2 dB (NEXT)	07/07/2026 09:58 AM
2E-V-045	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 10:08 AM
2E-V-048	PASS	TIA Cat 6 Perm. Link	170 ft	6.9 dB (NEXT)	07/07/2026 01:32 PM
2E-V-049	PASS	TIA Cat 6 Perm. Link	170 ft	6.3 dB (NEXT)	07/07/2026 01:29 PM
2E-V-050	PASS	TIA Cat 6 Perm. Link	149 ft	4.2 dB (NEXT)	07/07/2026 01:26 PM
2E-V-051	PASS	TIA Cat 6 Perm. Link	156 ft	5.9 dB (NEXT)	07/07/2026 01:24 PM
2E-V-052	PASS*	TIA Cat 6 Perm. Link	156 ft	0.6 dB (NEXT)	07/07/2026 12:21 PM
2E-V-053	PASS	TIA Cat 6 Perm. Link	165 ft	6.8 dB (NEXT)	07/07/2026 01:52 PM
2E-V-054	PASS	TIA Cat 6 Perm. Link	172 ft	7.6 dB (NEXT)	07/07/2026 01:55 PM
2E-V-055	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 01:58 PM
2E-V-056	PASS	TIA Cat 6 Perm. Link	151 ft	5.5 dB (NEXT)	07/07/2026 02:00 PM
2E-V-057	PASS	TIA Cat 6 Perm. Link	156 ft	6.4 dB (NEXT)	07/07/2026 02:03 PM
2E-V-058	PASS	TIA Cat 6 Perm. Link	158 ft	9.0 dB (NEXT)	07/07/2026 02:05 PM
2E-V-059	PASS	TIA Cat 6 Perm. Link	142 ft	5.9 dB (NEXT)	07/07/2026 09:48 AM
2E-V-060	PASS	TIA Cat 6 Perm. Link	138 ft	5.4 dB (NEXT)	07/07/2026 09:52 AM
2E-V-061	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 09:54 AM
2E-V-062	PASS	TIA Cat 6 Perm. Link	137 ft	6.2 dB (NEXT)	07/07/2026 09:44 AM
2E-V-063	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/07/2026 09:41 AM
2E-V-064	FAIL	TIA Cat 6 Perm. Link	124 ft	N/A	07/07/2026 09:36 AM
2E-V-065	PASS	TIA Cat 6 Perm. Link	123 ft	6.3 dB (NEXT)	07/07/2026 09:32 AM
2E-V-066	PASS	TIA Cat 6 Perm. Link	129 ft	6.2 dB (NEXT)	07/07/2026 09:29 AM
2E-V-067	PASS	TIA Cat 6 Perm. Link	137 ft	2.8 dB (NEXT)	07/07/2026 09:26 AM
2E-V-068	FAIL	TIA Cat 6 Perm. Link	112 ft	N/A	07/07/2026 09:22 AM
2E-V-069	FAIL	TIA Cat 6 Perm. Link	109 ft	N/A	07/07/2026 09:19 AM
2E-V-070	PASS	TIA Cat 6 Perm. Link	102 ft	7.3 dB (NEXT)	07/07/2026 09:15 AM
2E-V-071	FAIL	TIA Cat 6 Perm. Link	112 ft	N/A	07/07/2026 09:11 AM
2E-V-072	PASS	TIA Cat 6 Perm. Link	120 ft	6.8 dB (NEXT)	07/07/2026 09:09 AM
2E-V-073	PASS	TIA Cat 6 Perm. Link	103 ft	6.6 dB (NEXT)	07/07/2026 08:59 AM
2E-V-074	PASS	TIA Cat 6 Perm. Link	105 ft	6.3 dB (NEXT)	07/07/2026 08:56 AM
2E-V-076	PASS	TIA Cat 6 Perm. Link	112 ft	7.0 dB (NEXT)	07/07/2026 12:12 PM
2E-V-077	PASS	TIA Cat 6 Perm. Link	108 ft	5.2 dB (NEXT)	07/07/2026 12:06 PM
2E-V-078	FAIL	TIA Cat 6 Perm. Link	100 ft	-9.0 dB (NEXT)	07/07/2026 12:05 PM
2E-V-080	FAIL	TIA Cat 6 Perm. Link	103 ft	N/A	07/07/2026 12:16 PM
2E-V-081	PASS	TIA Cat 6 Perm. Link	75 ft	5.6 dB (NEXT)	07/07/2026 08:25 AM
2E-V-082	PASS	TIA Cat 6 Perm. Link	86 ft	5.9 dB (NEXT)	07/07/2026 08:33 AM
2E-V-083	PASS	TIA Cat 6 Perm. Link	92 ft	1.1 dB (NEXT)	07/07/2026 08:36 AM
2E-V-084	PASS	TIA Cat 6 Perm. Link	89 ft	3.6 dB (NEXT)	07/07/2026 08:37 AM
2E-V-085	PASS	TIA Cat 6 Perm. Link	82 ft	4.9 dB (NEXT)	07/07/2026 08:44 AM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2E-V-086	FAIL	TIA Cat 6 Perm. Link	76 ft	N/A	07/07/2026 08:48 AM
2E-V-087	PASS	TIA Cat 6 Perm. Link	140 ft	7.2 dB (NEXT)	07/09/2026 11:31 AM
2E-V-088	PASS	TIA Cat 6 Perm. Link	140 ft	3.6 dB (NEXT)	07/09/2026 11:35 AM
2E-V-089	PASS	TIA Cat 6 Perm. Link	140 ft	4.9 dB (NEXT)	07/09/2026 11:35 AM
2E-V-090	PASS	TIA Cat 6 Perm. Link	140 ft	5.2 dB (NEXT)	07/09/2026 11:36 AM
2E-V-091	PASS	TIA Cat 6 Perm. Link	140 ft	6.5 dB (NEXT)	07/09/2026 11:36 AM
2E-V-092	PASS	TIA Cat 6 Perm. Link	121 ft	4.5 dB (NEXT)	07/09/2026 11:27 AM
2E-V-093	PASS	TIA Cat 6 Perm. Link	123 ft	6.5 dB (NEXT)	07/09/2026 11:29 AM
2E-V-094	PASS	TIA Cat 6 Perm. Link	123 ft	5.4 dB (NEXT)	07/09/2026 11:29 AM
2E-V-095	PASS	TIA Cat 6 Perm. Link	124 ft	6.7 dB (NEXT)	07/09/2026 11:29 AM
2E-V-096	PASS	TIA Cat 6 Perm. Link	123 ft	6.4 dB (NEXT)	07/09/2026 11:30 AM
2E-V-097	FAIL	TIA Cat 6 Perm. Link	123 ft	N/A	07/09/2026 11:30 AM
2E-V-098	PASS	TIA Cat 6 Perm. Link	110 ft	4.4 dB (NEXT)	07/09/2026 11:21 AM
2E-V-099	PASS	TIA Cat 6 Perm. Link	110 ft	6.8 dB (NEXT)	07/09/2026 11:24 AM
2E-V-100	PASS	TIA Cat 6 Perm. Link	110 ft	6.2 dB (NEXT)	07/09/2026 11:25 AM
2E-V-101	PASS	TIA Cat 6 Perm. Link	109 ft	5.2 dB (NEXT)	07/09/2026 11:25 AM
2E-V-102	PASS	TIA Cat 6 Perm. Link	110 ft	5.7 dB (NEXT)	07/09/2026 11:25 AM
2E-V-103	PASS	TIA Cat 6 Perm. Link	110 ft	6.8 dB (NEXT)	07/09/2026 11:26 AM
2E-V-104	PASS	TIA Cat 6 Perm. Link	123 ft	3.5 dB (NEXT)	07/09/2026 12:02 PM
2E-V-105	PASS	TIA Cat 6 Perm. Link	152 ft	5.6 dB (NEXT)	07/09/2026 11:59 AM
2E-V-106	PASS	TIA Cat 6 Perm. Link	151 ft	6.3 dB (NEXT)	07/09/2026 11:59 AM
2E-V-107	PASS	TIA Cat 6 Perm. Link	152 ft	4.6 dB (NEXT)	07/09/2026 11:59 AM
2E-V-108	PASS	TIA Cat 6 Perm. Link	151 ft	4.9 dB (NEXT)	07/09/2026 12:00 PM
2E-V-109	PASS	TIA Cat 6 Perm. Link	152 ft	7.6 dB (NEXT)	07/09/2026 12:00 PM
2E-V-110	FAIL	TIA Cat 6 Perm. Link	151 ft	N/A	07/09/2026 12:01 PM
2E-V-112	PASS	TIA Cat 6 Perm. Link	130 ft	5.8 dB (NEXT)	07/10/2026 08:25 AM
2E-V-113	PASS	TIA Cat 6 Perm. Link	130 ft	5.9 dB (NEXT)	07/10/2026 08:19 AM
2E-V-115	PASS	TIA Cat 6 Perm. Link	149 ft	5.9 dB (NEXT)	07/10/2026 08:12 AM
2E-V-116	PASS	TIA Cat 6 Perm. Link	147 ft	7.0 dB (NEXT)	07/10/2026 08:07 AM
2E-V-117	PASS*	TIA Cat 6 Perm. Link	149 ft	0.5 dB (NEXT)	07/10/2026 08:06 AM
2E-V-118	PASS	TIA Cat 6 Perm. Link	150 ft	6.2 dB (NEXT)	07/10/2026 08:04 AM
2E-V-119	PASS	TIA Cat 6 Perm. Link	155 ft	7.9 dB (NEXT)	07/08/2026 07:22 AM
2E-V-120	PASS	TIA Cat 6 Perm. Link	162 ft	5.9 dB (NEXT)	07/08/2026 07:43 AM
2E-V-121	PASS	TIA Cat 6 Perm. Link	161 ft	1.5 dB (NEXT)	07/08/2026 10:43 AM
2E-V-123	PASS	TIA Cat 6 Perm. Link	118 ft	7.5 dB (NEXT)	07/10/2026 07:05 AM
2E-V-124	PASS	TIA Cat 6 Perm. Link	118 ft	3.6 dB (NEXT)	07/10/2026 06:59 AM
2E-V-125	PASS	TIA Cat 6 Perm. Link	95 ft	3.8 dB (NEXT)	07/10/2026 08:30 AM
2E-V-126	PASS	TIA Cat 6 Perm. Link	92 ft	7.0 dB (NEXT)	07/10/2026 08:28 AM
2E-V-127	PASS	TIA Cat 6 Perm. Link	82 ft	1.1 dB (NEXT)	07/10/2026 08:00 AM
2E-V-128	PASS	TIA Cat 6 Perm. Link	86 ft	6.3 dB (NEXT)	07/10/2026 07:57 AM
2E-V-129	PASS*	TIA Cat 6 Perm. Link	36 ft	0.0 dB (NEXT)	07/10/2026 08:34 AM
2E-V-130	PASS	TIA Cat 6 Perm. Link	39 ft	2.2 dB (NEXT)	07/10/2026 08:40 AM
2E-V-134	PASS	TIA Cat 6 Perm. Link	82 ft	3.7 dB (NEXT)	07/07/2026 09:02 AM

Total Length:	16349 ft
Number of Reports:	121
Number of Passing Reports:	94
Number of Failing Reports:	27
Number of Warning Reports:	0
Documentation Only:	0

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2W-D-001A	FAIL	TIA Cat 6 Perm. Link	143 ft	N/A	07/09/2026 01:54 PM
2W-D-001B	PASS	TIA Cat 6 Perm. Link	144 ft	5.4 dB (NEXT)	07/09/2026 01:53 PM
2W-D-002A	PASS	TIA Cat 6 Perm. Link	140 ft	3.4 dB (NEXT)	07/09/2026 01:51 PM
2W-D-002B	PASS	TIA Cat 6 Perm. Link	141 ft	2.5 dB (NEXT)	07/09/2026 01:51 PM
2W-D-003A	PASS	TIA Cat 6 Perm. Link	142 ft	4.9 dB (NEXT)	07/09/2026 06:29 AM
2W-D-003B	PASS	TIA Cat 6 Perm. Link	144 ft	7.3 dB (NEXT)	07/09/2026 06:30 AM
2W-D-004A	PASS	TIA Cat 6 Perm. Link	141 ft	5.6 dB (NEXT)	07/09/2026 06:21 AM
2W-D-004B	PASS	TIA Cat 6 Perm. Link	140 ft	7.7 dB (NEXT)	07/09/2026 06:21 AM
2W-D-005A	PASS	TIA Cat 6 Perm. Link	133 ft	3.7 dB (NEXT)	07/09/2026 06:19 AM
2W-D-005B	FAIL	TIA Cat 6 Perm. Link	134 ft	-1.3 dB (NEXT)	07/09/2026 06:20 AM
2W-D-006A	PASS	TIA Cat 6 Perm. Link	141 ft	6.8 dB (NEXT)	07/09/2026 06:17 AM
2W-D-006B	PASS	TIA Cat 6 Perm. Link	142 ft	8.1 dB (NEXT)	07/09/2026 06:17 AM
2W-D-007A	PASS	TIA Cat 6 Perm. Link	133 ft	3.1 dB (NEXT)	07/09/2026 06:15 AM
2W-D-007B	PASS	TIA Cat 6 Perm. Link	132 ft	7.0 dB (NEXT)	07/09/2026 06:15 AM
2W-D-008A	PASS	TIA Cat 6 Perm. Link	131 ft	2.2 dB (NEXT)	07/10/2026 06:51 AM
2W-D-008B	PASS	TIA Cat 6 Perm. Link	131 ft	5.2 dB (NEXT)	07/10/2026 06:51 AM
2W-D-009A	FAIL	TIA Cat 6 Perm. Link	138 ft	N/A	07/08/2026 01:48 PM
2W-D-009B	PASS	TIA Cat 6 Perm. Link	137 ft	5.0 dB (NEXT)	07/08/2026 01:49 PM
2W-D-010A	PASS	TIA Cat 6 Perm. Link	144 ft	6.7 dB (NEXT)	07/08/2026 01:44 PM
2W-D-010B	PASS	TIA Cat 6 Perm. Link	145 ft	6.9 dB (NEXT)	07/08/2026 01:46 PM
2W-D-011A	PASS	TIA Cat 6 Perm. Link	94 ft	6.0 dB (NEXT)	07/08/2026 01:42 PM
2W-D-011B	PASS	TIA Cat 6 Perm. Link	96 ft	8.5 dB (NEXT)	07/08/2026 01:42 PM
2W-D-012A	PASS	TIA Cat 6 Perm. Link	94 ft	4.0 dB (NEXT)	07/08/2026 01:37 PM
2W-D-013A	PASS	TIA Cat 6 Perm. Link	132 ft	4.4 dB (NEXT)	07/08/2026 01:53 PM
2W-D-013B	PASS*	TIA Cat 6 Perm. Link	132 ft	7.3 dB (NEXT)	07/08/2026 01:54 PM
2W-D-014A	PASS	TIA Cat 6 Perm. Link	138 ft	3.7 dB (NEXT)	07/09/2026 06:11 AM
2W-D-014B	PASS	TIA Cat 6 Perm. Link	138 ft	7.3 dB (NEXT)	07/09/2026 06:13 AM
2W-D-015A	PASS	TIA Cat 6 Perm. Link	145 ft	7.6 dB (NEXT)	07/08/2026 01:33 PM
2W-D-015B	PASS	TIA Cat 6 Perm. Link	144 ft	4.1 dB (NEXT)	07/08/2026 01:34 PM
2W-D-016A	PASS	TIA Cat 6 Perm. Link	94 ft	8.0 dB (NEXT)	07/08/2026 01:30 PM
2W-D-016B	PASS	TIA Cat 6 Perm. Link	94 ft	6.3 dB (NEXT)	07/08/2026 01:31 PM
2W-D-017A	PASS	TIA Cat 6 Perm. Link	96 ft	6.0 dB (NEXT)	07/08/2026 01:27 PM
2W-D-017B	PASS	TIA Cat 6 Perm. Link	96 ft	2.8 dB (NEXT)	07/08/2026 01:27 PM
2W-D-018A	PASS	TIA Cat 6 Perm. Link	112 ft	7.4 dB (NEXT)	07/08/2026 01:22 PM
2W-D-018B	PASS	TIA Cat 6 Perm. Link	113 ft	4.0 dB (NEXT)	07/08/2026 01:22 PM
2W-D-019A	PASS	TIA Cat 6 Perm. Link	103 ft	0.9 dB (NEXT)	07/08/2026 01:24 PM
2W-D-019B	PASS	TIA Cat 6 Perm. Link	103 ft	2.7 dB (NEXT)	07/08/2026 01:25 PM
2W-D-020A	PASS	TIA Cat 6 Perm. Link	107 ft	5.5 dB (NEXT)	07/09/2026 06:37 AM
2W-D-020B	PASS	TIA Cat 6 Perm. Link	107 ft	6.4 dB (NEXT)	07/09/2026 06:38 AM
2W-D-021A	PASS	TIA Cat 6 Perm. Link	100 ft	2.2 dB (NEXT)	07/09/2026 06:34 AM
2W-D-021B	PASS	TIA Cat 6 Perm. Link	102 ft	6.9 dB (NEXT)	07/09/2026 06:35 AM
2W-D-022A	PASS	TIA Cat 6 Perm. Link	101 ft	7.6 dB (NEXT)	07/09/2026 06:39 AM
2W-D-022B	PASS	TIA Cat 6 Perm. Link	101 ft	7.3 dB (NEXT)	07/09/2026 06:42 AM
2W-D-023A	PASS	TIA Cat 6 Perm. Link	107 ft	8.3 dB (NEXT)	07/09/2026 06:47 AM
2W-D-023B	PASS	TIA Cat 6 Perm. Link	107 ft	2.7 dB (NEXT)	07/09/2026 06:48 AM
2W-D-025A	PASS	TIA Cat 6 Perm. Link	112 ft	6.0 dB (NEXT)	07/09/2026 06:53 AM
2W-D-025B	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/09/2026 06:54 AM
2W-D-026A	PASS	TIA Cat 6 Perm. Link	153 ft	6.7 dB (NEXT)	07/09/2026 01:43 PM
2W-D-026B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 01:45 PM
2W-D-027A	PASS	TIA Cat 6 Perm. Link	96 ft	5.0 dB (NEXT)	07/09/2026 07:00 AM
2W-D-027B	FAIL	TIA Cat 6 Perm. Link	96 ft	N/A	07/09/2026 07:01 AM
2W-D-028A	PASS	TIA Cat 6 Perm. Link	96 ft	6.6 dB (NEXT)	07/09/2026 07:03 AM
2W-D-028B	PASS	TIA Cat 6 Perm. Link	96 ft	2.6 dB (NEXT)	07/09/2026 07:04 AM
2W-D-029A	PASS	TIA Cat 6 Perm. Link	104 ft	4.1 dB (NEXT)	07/09/2026 07:05 AM
2W-D-029B	PASS	TIA Cat 6 Perm. Link	104 ft	6.1 dB (NEXT)	07/09/2026 07:07 AM
2W-D-030A	PASS	TIA Cat 6 Perm. Link	82 ft	4.8 dB (NEXT)	07/09/2026 07:16 AM
2W-D-030B	PASS	TIA Cat 6 Perm. Link	83 ft	3.6 dB (NEXT)	07/09/2026 07:17 AM
2W-D-031A	PASS	TIA Cat 6 Perm. Link	88 ft	6.9 dB (NEXT)	07/09/2026 07:08 AM
2W-D-031B	PASS	TIA Cat 6 Perm. Link	88 ft	5.1 dB (NEXT)	07/09/2026 07:09 AM
2W-D-036A	FAIL	TIA Cat 6 Perm. Link	52 ft	N/A	07/09/2026 12:32 PM
2W-D-036B	PASS	TIA Cat 6 Perm. Link	51 ft	3.7 dB (NEXT)	07/09/2026 12:32 PM
2W-D-037A	PASS	TIA Cat 6 Perm. Link	51 ft	5.7 dB (NEXT)	07/10/2026 06:16 AM
2W-D-037B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/10/2026 06:16 AM
2W-D-038A	PASS	TIA Cat 6 Perm. Link	52 ft	5.4 dB (NEXT)	07/09/2026 12:34 PM
2W-D-038B	PASS	TIA Cat 6 Perm. Link	51 ft	3.8 dB (NEXT)	07/09/2026 12:35 PM
2W-D-039A	PASS	TIA Cat 6 Perm. Link	89 ft	6.6 dB (NEXT)	07/09/2026 07:34 AM
2W-D-039B	PASS	TIA Cat 6 Perm. Link	89 ft	4.2 dB (NEXT)	07/09/2026 07:35 AM
2W-D-040A	PASS	TIA Cat 6 Perm. Link	85 ft	6.7 dB (NEXT)	07/09/2026 07:36 AM
2W-D-040B	PASS	TIA Cat 6 Perm. Link	84 ft	6.9 dB (NEXT)	07/09/2026 07:37 AM
2W-D-041A	PASS	TIA Cat 6 Perm. Link	78 ft	2.9 dB (NEXT)	07/09/2026 07:38 AM
2W-D-041B	PASS	TIA Cat 6 Perm. Link	79 ft	4.8 dB (NEXT)	07/09/2026 07:39 AM
2W-D-042A	FAIL	TIA Cat 6 Perm. Link	63 ft	-1.8 dB (NEXT)	07/09/2026 12:38 PM
2W-D-042B	PASS	TIA Cat 6 Perm. Link	64 ft	6.2 dB (NEXT)	07/09/2026 12:39 PM
2W-D-043A	PASS	TIA Cat 6 Perm. Link	65 ft	2.2 dB (NEXT)	07/09/2026 07:51 AM
2W-D-043B	PASS	TIA Cat 6 Perm. Link	64 ft	5.0 dB (NEXT)	07/09/2026 07:51 AM
2W-D-044A	PASS	TIA Cat 6 Perm. Link	72 ft	7.0 dB (NEXT)	07/09/2026 07:48 AM
2W-D-044B	PASS	TIA Cat 6 Perm. Link	72 ft	5.6 dB (NEXT)	07/09/2026 07:48 AM
2W-D-045A	FAIL	TIA Cat 6 Perm. Link	92 ft	-0.4 dB (NEXT)	07/09/2026 07:57 AM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2W-D-045B	PASS	TIA Cat 6 Perm. Link	93 ft	7.5 dB (NEXT)	07/09/2026 07:57 AM
2W-D-046A	PASS	TIA Cat 6 Perm. Link	98 ft	2.0 dB (NEXT)	07/09/2026 07:41 AM
2W-D-046B	PASS	TIA Cat 6 Perm. Link	98 ft	7.6 dB (NEXT)	07/09/2026 07:42 AM
2W-D-047A	PASS	TIA Cat 6 Perm. Link	104 ft	7.3 dB (NEXT)	07/09/2026 07:44 AM
2W-D-047B	FAIL	TIA Cat 6 Perm. Link	105 ft	-0.9 dB (NEXT)	07/09/2026 07:46 AM
2W-D-048A	PASS	TIA Cat 6 Perm. Link	94 ft	4.8 dB (NEXT)	07/08/2026 01:09 PM
2W-D-048B	PASS	TIA Cat 6 Perm. Link	94 ft	8.6 dB (NEXT)	07/08/2026 01:10 PM
2W-D-050A	PASS	TIA Cat 6 Perm. Link	108 ft	7.7 dB (NEXT)	07/08/2026 01:13 PM
2W-D-050B	PASS	TIA Cat 6 Perm. Link	109 ft	2.7 dB (NEXT)	07/08/2026 01:13 PM
2W-D-051A	PASS	TIA Cat 6 Perm. Link	114 ft	3.4 dB (NEXT)	07/08/2026 01:16 PM
2W-D-051B	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/08/2026 01:17 PM
2W-D-053A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 12:43 PM
2W-D-053B	PASS	TIA Cat 6 Perm. Link	100 ft	6.3 dB (NEXT)	07/09/2026 12:44 PM
2W-D-054A	PASS	TIA Cat 6 Perm. Link	94 ft	5.6 dB (NEXT)	07/08/2026 01:02 PM
2W-D-054B	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/08/2026 01:03 PM
2W-D-055A	PASS	TIA Cat 6 Perm. Link	96 ft	4.4 dB (NEXT)	07/08/2026 12:58 PM
2W-D-055B	PASS	TIA Cat 6 Perm. Link	96 ft	5.2 dB (NEXT)	07/08/2026 12:58 PM
2W-D-056A	PASS	TIA Cat 6 Perm. Link	103 ft	5.5 dB (NEXT)	07/08/2026 12:53 PM
2W-D-056B	PASS	TIA Cat 6 Perm. Link	103 ft	4.1 dB (NEXT)	07/08/2026 12:54 PM
2W-D-057A	FAIL	TIA Cat 6 Perm. Link	115 ft	N/A	07/09/2026 01:01 PM
2W-D-057B	FAIL	TIA Cat 6 Perm. Link	115 ft	N/A	07/09/2026 01:06 PM
2W-D-058A	FAIL	TIA Cat 6 Perm. Link	108 ft	N/A	07/09/2026 12:58 PM
2W-D-058B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 01:00 PM
2W-D-059A	FAIL	TIA Cat 6 Perm. Link	102 ft	N/A	07/09/2026 12:51 PM
2W-D-059B	FAIL	TIA Cat 6 Perm. Link	101 ft	N/A	07/09/2026 12:51 PM
2W-D-060A	PASS	TIA Cat 6 Perm. Link	92 ft	3.8 dB (NEXT)	07/09/2026 01:15 PM
2W-D-060B	PASS	TIA Cat 6 Perm. Link	92 ft	8.1 dB (NEXT)	07/09/2026 01:15 PM
2W-D-061A	PASS	TIA Cat 6 Perm. Link	100 ft	6.4 dB (NEXT)	07/09/2026 01:12 PM
2W-D-061B	PASS	TIA Cat 6 Perm. Link	99 ft	3.4 dB (NEXT)	07/09/2026 01:12 PM
2W-D-062A	PASS	TIA Cat 6 Perm. Link	106 ft	3.3 dB (NEXT)	07/09/2026 01:09 PM
2W-D-062B	FAIL	TIA Cat 6 Perm. Link	105 ft	N/A	07/09/2026 01:10 PM
2W-D-063A	PASS	TIA Cat 6 Perm. Link	132 ft	1.7 dB (NEXT)	07/09/2026 02:03 PM
2W-D-063B	PASS	TIA Cat 6 Perm. Link	132 ft	6.9 dB (NEXT)	07/09/2026 02:03 PM
2W-D-064A	PASS	TIA Cat 6 Perm. Link	124 ft	4.4 dB (NEXT)	07/09/2026 02:06 PM
2W-D-064B	PASS	TIA Cat 6 Perm. Link	123 ft	3.8 dB (NEXT)	07/09/2026 02:06 PM
2W-D-065A	PASS	TIA Cat 6 Perm. Link	114 ft	2.9 dB (NEXT)	07/09/2026 12:26 PM
2W-D-065B	PASS	TIA Cat 6 Perm. Link	113 ft	2.5 dB (NEXT)	07/09/2026 12:26 PM
2W-D-066A	PASS	TIA Cat 6 Perm. Link	114 ft	5.7 dB (NEXT)	07/09/2026 12:20 PM
2W-D-066B	PASS	TIA Cat 6 Perm. Link	114 ft	7.7 dB (NEXT)	07/09/2026 12:16 PM
2W-D-067A	FAIL	TIA Cat 6 Perm. Link	140 ft	N/A	07/09/2026 12:15 PM
2W-D-068A	FAIL	TIA Cat 6 Perm. Link	120 ft	-3.1 dB (NEXT)	07/09/2026 12:12 PM
2W-D-068B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 12:13 PM
2W-D-069A	PASS	TIA Cat 6 Perm. Link	151 ft	1.4 dB (NEXT)	07/09/2026 10:10 AM
2W-D-069B	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/09/2026 10:12 AM
2W-D-070A	PASS	TIA Cat 6 Perm. Link	151 ft	5.6 dB (NEXT)	07/09/2026 09:58 AM
2W-D-070B	PASS	TIA Cat 6 Perm. Link	151 ft	5.7 dB (NEXT)	07/09/2026 10:02 AM
2W-D-071A	PASS	TIA Cat 6 Perm. Link	145 ft	1.4 dB (NEXT)	07/09/2026 10:12 AM
2W-D-071B	PASS	TIA Cat 6 Perm. Link	145 ft	7.4 dB (NEXT)	07/09/2026 10:15 AM
2W-D-072A	PASS	TIA Cat 6 Perm. Link	163 ft	6.8 dB (NEXT)	07/09/2026 09:44 AM
2W-D-072B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 09:44 AM
2W-D-073A	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 09:47 AM
2W-D-073B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 09:49 AM
2W-D-074A	PASS	TIA Cat 6 Perm. Link	172 ft	5.8 dB (NEXT)	07/09/2026 09:33 AM
2W-D-074B	PASS	TIA Cat 6 Perm. Link	172 ft	5.7 dB (NEXT)	07/09/2026 09:33 AM
2W-D-075A	PASS	TIA Cat 6 Perm. Link	174 ft	2.2 dB (NEXT)	07/09/2026 09:35 AM
2W-D-075B	PASS	TIA Cat 6 Perm. Link	170 ft	4.2 dB (NEXT)	07/09/2026 09:37 AM
2W-D-076A	PASS	TIA Cat 6 Perm. Link	162 ft	6.9 dB (NEXT)	07/09/2026 09:39 AM
2W-D-076B	FAIL	TIA Cat 6 Perm. Link	162 ft	N/A	07/09/2026 09:40 AM
2W-D-077A	PASS	TIA Cat 6 Perm. Link	100 ft	2.4 dB (NEXT)	07/09/2026 02:10 PM
2W-D-077B	PASS	TIA Cat 6 Perm. Link	99 ft	6.4 dB (NEXT)	07/09/2026 02:10 PM
2W-D-078A	FAIL	TIA Cat 6 Perm. Link	194 ft	-0.1 dB (NEXT)	07/09/2026 08:09 AM
2W-D-078B	PASS	TIA Cat 6 Perm. Link	194 ft	5.0 dB (NEXT)	07/09/2026 08:09 AM
2W-D-079A	PASS	TIA Cat 6 Perm. Link	216 ft	4.1 dB (NEXT)	07/09/2026 08:06 AM
2W-D-079B	PASS	TIA Cat 6 Perm. Link	216 ft	7.8 dB (NEXT)	07/09/2026 08:06 AM
2W-D-080A	PASS	TIA Cat 6 Perm. Link	209 ft	5.8 dB (NEXT)	07/09/2026 08:14 AM
2W-D-080B	PASS*	TIA Cat 6 Perm. Link	209 ft	0.6 dB (NEXT)	07/09/2026 08:15 AM
2W-D-081A	PASS	TIA Cat 6 Perm. Link	217 ft	3.9 dB (NEXT)	07/09/2026 09:09 AM
2W-D-081B	PASS	TIA Cat 6 Perm. Link	217 ft	6.9 dB (NEXT)	07/09/2026 09:09 AM
2W-D-082A	PASS	TIA Cat 6 Perm. Link	210 ft	3.8 dB (NEXT)	07/09/2026 08:59 AM
2W-D-082B	FAIL	TIA Cat 6 Perm. Link	212 ft	N/A	07/09/2026 09:04 AM
2W-D-083A	PASS	TIA Cat 6 Perm. Link	214 ft	7.0 dB (NEXT)	07/09/2026 08:28 AM
2W-D-083B	PASS	TIA Cat 6 Perm. Link	215 ft	7.1 dB (NEXT)	07/09/2026 08:29 AM
2W-D-084A	PASS	TIA Cat 6 Perm. Link	212 ft	4.1 dB (NEXT)	07/09/2026 08:30 AM
2W-D-084B	PASS	TIA Cat 6 Perm. Link	211 ft	5.9 dB (NEXT)	07/09/2026 08:31 AM
2W-D-085A	PASS	TIA Cat 6 Perm. Link	212 ft	4.3 dB (NEXT)	07/10/2026 08:35 AM
2W-D-085B	PASS	TIA Cat 6 Perm. Link	211 ft	6.0 dB (NEXT)	07/10/2026 08:35 AM
2W-D-086A	PASS	TIA Cat 6 Perm. Link	204 ft	6.4 dB (NEXT)	07/09/2026 08:35 AM
2W-D-086B	PASS	TIA Cat 6 Perm. Link	203 ft	6.4 dB (NEXT)	07/09/2026 08:36 AM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2W-D-087A	PASS	TIA Cat 6 Perm. Link	190 ft	4.4 dB (NEXT)	07/09/2026 08:53 AM
2W-D-087B	PASS	TIA Cat 6 Perm. Link	189 ft	6.1 dB (NEXT)	07/09/2026 08:54 AM
2W-D-088A	PASS	TIA Cat 6 Perm. Link	197 ft	5.9 dB (NEXT)	07/09/2026 09:05 AM
2W-D-088B	PASS	TIA Cat 6 Perm. Link	198 ft	7.7 dB (NEXT)	07/09/2026 09:08 AM
2W-D-089A	PASS	TIA Cat 6 Perm. Link	202 ft	7.1 dB (NEXT)	07/09/2026 08:24 AM
2W-D-089B	PASS	TIA Cat 6 Perm. Link	202 ft	3.8 dB (NEXT)	07/09/2026 08:25 AM
2W-D-090A	PASS	TIA Cat 6 Perm. Link	204 ft	7.1 dB (NEXT)	07/09/2026 08:18 AM
2W-D-090B	PASS	TIA Cat 6 Perm. Link	203 ft	6.7 dB (NEXT)	07/09/2026 08:18 AM
2W-D-091A	PASS	TIA Cat 6 Perm. Link	214 ft	1.2 dB (NEXT)	07/09/2026 08:42 AM
2W-D-091B	PASS	TIA Cat 6 Perm. Link	215 ft	2.2 dB (NEXT)	07/09/2026 08:42 AM
2W-D-092A	PASS	TIA Cat 6 Perm. Link	228 ft	5.3 dB (NEXT)	07/09/2026 08:40 AM
2W-D-092B	PASS	TIA Cat 6 Perm. Link	226 ft	5.6 dB (NEXT)	07/09/2026 08:40 AM
2W-D-094A	PASS	TIA Cat 6 Perm. Link	167 ft	7.7 dB (NEXT)	07/08/2026 12:42 PM
2W-D-094B	PASS	TIA Cat 6 Perm. Link	166 ft	5.7 dB (NEXT)	07/08/2026 12:42 PM
2W-D-095A	PASS	TIA Cat 6 Perm. Link	166 ft	5.2 dB (NEXT)	07/09/2026 09:20 AM
2W-D-095B	PASS	TIA Cat 6 Perm. Link	166 ft	5.4 dB (NEXT)	07/09/2026 09:21 AM
2W-D-096A	PASS	TIA Cat 6 Perm. Link	167 ft	6.0 dB (NEXT)	07/09/2026 09:18 AM
2W-D-096B	PASS	TIA Cat 6 Perm. Link	166 ft	3.1 dB (NEXT)	07/09/2026 09:18 AM
2W-D-097A	PASS	TIA Cat 6 Perm. Link	165 ft	6.3 dB (NEXT)	07/09/2026 09:11 AM
2W-D-097B	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/09/2026 09:12 AM
2W-D-098A	PASS	TIA Cat 6 Perm. Link	165 ft	3.5 dB (NEXT)	07/09/2026 09:15 AM
2W-D-098B	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 09:16 AM
2W-D-099A	PASS	TIA Cat 6 Perm. Link	79 ft	2.1 dB (NEXT)	07/08/2026 08:18 AM
2W-D-099B	PASS	TIA Cat 6 Perm. Link	78 ft	5.1 dB (NEXT)	07/08/2026 08:17 AM
2W-D-100A	FAIL	TIA Cat 6 Perm. Link	91 ft	N/A	07/08/2026 08:20 AM
2W-D-100B	PASS	TIA Cat 6 Perm. Link	92 ft	2.4 dB (NEXT)	07/08/2026 08:20 AM
2W-D-101A	PASS	TIA Cat 6 Perm. Link	91 ft	3.8 dB (NEXT)	07/08/2026 08:22 AM
2W-D-101B	PASS	TIA Cat 6 Perm. Link	92 ft	4.8 dB (NEXT)	07/08/2026 08:23 AM
2W-D-102A	PASS	TIA Cat 6 Perm. Link	94 ft	3.6 dB (NEXT)	07/08/2026 08:26 AM
2W-D-102B	PASS	TIA Cat 6 Perm. Link	93 ft	3.0 dB (NEXT)	07/08/2026 08:26 AM
2W-D-103A	PASS	TIA Cat 6 Perm. Link	92 ft	4.9 dB (NEXT)	07/08/2026 08:28 AM
2W-D-103B	PASS	TIA Cat 6 Perm. Link	93 ft	6.3 dB (NEXT)	07/08/2026 08:28 AM
2W-D-104A	PASS	TIA Cat 6 Perm. Link	85 ft	5.6 dB (NEXT)	07/08/2026 08:30 AM
2W-D-104B	PASS	TIA Cat 6 Perm. Link	86 ft	3.1 dB (NEXT)	07/08/2026 08:31 AM
2W-D-105A	PASS	TIA Cat 6 Perm. Link	85 ft	4.8 dB (NEXT)	07/08/2026 08:34 AM
2W-D-105B	PASS	TIA Cat 6 Perm. Link	85 ft	4.7 dB (NEXT)	07/08/2026 08:35 AM
2W-D-106A	PASS	TIA Cat 6 Perm. Link	74 ft	6.1 dB (NEXT)	07/08/2026 08:37 AM
2W-D-106B	FAIL	TIA Cat 6 Perm. Link	74 ft	N/A	07/08/2026 08:38 AM
2W-D-107A	PASS	TIA Cat 6 Perm. Link	81 ft	5.4 dB (NEXT)	07/08/2026 08:41 AM
2W-D-107B	PASS	TIA Cat 6 Perm. Link	80 ft	5.0 dB (NEXT)	07/08/2026 08:41 AM
2W-D-108A	PASS	TIA Cat 6 Perm. Link	83 ft	6.4 dB (NEXT)	07/08/2026 08:44 AM
2W-D-108B	PASS	TIA Cat 6 Perm. Link	83 ft	6.7 dB (NEXT)	07/08/2026 08:44 AM
2W-D-109A	PASS	TIA Cat 6 Perm. Link	94 ft	7.6 dB (NEXT)	07/08/2026 08:58 AM
2W-D-109B	PASS	TIA Cat 6 Perm. Link	94 ft	1.8 dB (NEXT)	07/08/2026 08:58 AM
2W-D-110A	PASS	TIA Cat 6 Perm. Link	100 ft	3.0 dB (NEXT)	07/08/2026 09:08 AM
2W-D-110B	FAIL	TIA Cat 6 Perm. Link	100 ft	-1.7 dB (NEXT)	07/08/2026 09:09 AM
2W-D-111A	PASS	TIA Cat 6 Perm. Link	106 ft	3.6 dB (NEXT)	07/08/2026 09:13 AM
2W-D-111B	PASS	TIA Cat 6 Perm. Link	107 ft	6.4 dB (NEXT)	07/08/2026 09:16 AM
2W-D-112A	PASS	TIA Cat 6 Perm. Link	86 ft	5.3 dB (NEXT)	07/08/2026 08:53 AM
2W-D-112B	PASS	TIA Cat 6 Perm. Link	87 ft	4.9 dB (NEXT)	07/08/2026 08:55 AM
2W-D-113A	PASS	TIA Cat 6 Perm. Link	93 ft	5.6 dB (NEXT)	07/08/2026 08:51 AM
2W-D-113B	PASS	TIA Cat 6 Perm. Link	92 ft	5.6 dB (NEXT)	07/08/2026 08:51 AM
2W-D-114A	PASS	TIA Cat 6 Perm. Link	100 ft	3.7 dB (NEXT)	07/08/2026 08:48 AM
2W-D-114B	PASS	TIA Cat 6 Perm. Link	100 ft	3.2 dB (NEXT)	07/08/2026 08:49 AM
2W-D-115A	PASS	TIA Cat 6 Perm. Link	135 ft	2.7 dB (NEXT)	07/08/2026 09:05 AM
2W-D-115B	PASS	TIA Cat 6 Perm. Link	135 ft	5.7 dB (NEXT)	07/08/2026 09:06 AM
2W-D-116A	PASS	TIA Cat 6 Perm. Link	141 ft	3.2 dB (NEXT)	07/08/2026 09:03 AM
2W-D-116B	PASS	TIA Cat 6 Perm. Link	141 ft	6.2 dB (NEXT)	07/08/2026 09:04 AM
2W-D-117A	PASS	TIA Cat 6 Perm. Link	146 ft	5.5 dB (NEXT)	07/08/2026 09:23 AM
2W-D-117B	PASS	TIA Cat 6 Perm. Link	145 ft	2.4 dB (NEXT)	07/08/2026 09:24 AM
2W-D-118A	FAIL	TIA Cat 6 Perm. Link	145 ft	-2.2 dB (NEXT)	07/08/2026 11:35 AM
2W-D-118B	PASS	TIA Cat 6 Perm. Link	145 ft	4.5 dB (NEXT)	07/08/2026 11:35 AM
2W-D-119A	PASS	TIA Cat 6 Perm. Link	141 ft	5.8 dB (NEXT)	07/08/2026 11:41 AM
2W-D-120A	PASS	TIA Cat 6 Perm. Link	135 ft	6.1 dB (NEXT)	07/08/2026 11:38 AM
2W-D-120B	FAIL	TIA Cat 6 Perm. Link	134 ft	N/A	07/08/2026 11:39 AM
2W-D-121A	PASS	TIA Cat 6 Perm. Link	99 ft	3.9 dB (NEXT)	07/08/2026 12:01 PM
2W-D-121B	PASS	TIA Cat 6 Perm. Link	101 ft	3.7 dB (NEXT)	07/08/2026 12:02 PM
2W-D-122A	FAIL	TIA Cat 6 Perm. Link	93 ft	-2.0 dB (NEXT)	07/08/2026 11:45 AM
2W-D-122B	PASS	TIA Cat 6 Perm. Link	90 ft	4.1 dB (NEXT)	07/08/2026 11:45 AM
2W-D-123A	PASS	TIA Cat 6 Perm. Link	87 ft	3.8 dB (NEXT)	07/08/2026 11:47 AM
2W-D-123B	PASS	TIA Cat 6 Perm. Link	86 ft	2.0 dB (NEXT)	07/08/2026 11:48 AM
2W-D-124A	PASS	TIA Cat 6 Perm. Link	102 ft	6.6 dB (NEXT)	07/08/2026 11:49 AM
2W-D-124B	PASS	TIA Cat 6 Perm. Link	102 ft	6.2 dB (NEXT)	07/08/2026 11:50 AM
2W-D-125A	PASS	TIA Cat 6 Perm. Link	111 ft	5.4 dB (NEXT)	07/08/2026 11:53 AM
2W-D-125B	PASS	TIA Cat 6 Perm. Link	108 ft	5.4 dB (NEXT)	07/08/2026 11:53 AM
2W-D-126A	PASS	TIA Cat 6 Perm. Link	116 ft	7.2 dB (NEXT)	07/08/2026 11:57 AM
2W-D-126B	PASS	TIA Cat 6 Perm. Link	114 ft	2.6 dB (NEXT)	07/08/2026 11:57 AM
2W-D-127A	PASS	TIA Cat 6 Perm. Link	117 ft	5.5 dB (NEXT)	07/08/2026 12:12 PM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2W-D-127B	PASS	TIA Cat 6 Perm. Link	117 ft	6.2 dB (NEXT)	07/08/2026 12:12 PM
2W-D-128A	PASS	TIA Cat 6 Perm. Link	123 ft	3.7 dB (NEXT)	07/08/2026 12:15 PM
2W-D-128B	PASS	TIA Cat 6 Perm. Link	124 ft	5.2 dB (NEXT)	07/08/2026 12:16 PM
2W-D-129A	PASS	TIA Cat 6 Perm. Link	130 ft	5.8 dB (NEXT)	07/08/2026 12:19 PM
2W-D-129B	PASS	TIA Cat 6 Perm. Link	130 ft	5.1 dB (NEXT)	07/08/2026 12:19 PM
2W-D-130A	PASS	TIA Cat 6 Perm. Link	145 ft	7.4 dB (NEXT)	07/08/2026 12:22 PM
2W-D-130B	PASS	TIA Cat 6 Perm. Link	145 ft	5.3 dB (NEXT)	07/08/2026 12:22 PM
2W-D-132A	PASS	TIA Cat 6 Perm. Link	157 ft	7.6 dB (NEXT)	07/10/2026 06:37 AM
2W-D-132B	PASS	TIA Cat 6 Perm. Link	156 ft	3.5 dB (NEXT)	07/10/2026 06:38 AM
2W-D-133A	PASS	TIA Cat 6 Perm. Link	159 ft	8.7 dB (NEXT)	07/08/2026 12:36 PM
2W-D-133B	PASS	TIA Cat 6 Perm. Link	159 ft	6.1 dB (NEXT)	07/08/2026 12:37 PM
2W-D-134A	PASS	TIA Cat 6 Perm. Link	167 ft	6.0 dB (NEXT)	07/08/2026 12:34 PM
2W-D-134B	PASS	TIA Cat 6 Perm. Link	167 ft	5.8 dB (NEXT)	07/08/2026 12:34 PM
2W-D-135A	PASS	TIA Cat 6 Perm. Link	172 ft	7.7 dB (NEXT)	07/09/2026 01:26 PM
2W-D-135B	PASS	TIA Cat 6 Perm. Link	172 ft	1.6 dB (NEXT)	07/09/2026 01:26 PM
2W-D-136A	PASS	TIA Cat 6 Perm. Link	134 ft	7.4 dB (NEXT)	07/08/2026 11:31 AM
2W-D-136B	PASS	TIA Cat 6 Perm. Link	135 ft	6.8 dB (NEXT)	07/08/2026 11:32 AM
2W-D-137A	PASS	TIA Cat 6 Perm. Link	177 ft	5.6 dB (NEXT)	07/08/2026 11:28 AM
2W-D-137B	PASS	TIA Cat 6 Perm. Link	178 ft	7.7 dB (NEXT)	07/08/2026 11:28 AM
2W-D-138A	PASS	TIA Cat 6 Perm. Link	172 ft	6.2 dB (NEXT)	07/08/2026 11:26 AM
2W-D-138B	PASS	TIA Cat 6 Perm. Link	174 ft	6.0 dB (NEXT)	07/08/2026 11:27 AM
2W-D-139A	PASS	TIA Cat 6 Perm. Link	169 ft	6.2 dB (NEXT)	07/08/2026 11:24 AM
2W-D-139B	PASS	TIA Cat 6 Perm. Link	167 ft	6.0 dB (NEXT)	07/08/2026 11:25 AM
2W-D-140A	PASS	TIA Cat 6 Perm. Link	162 ft	5.7 dB (NEXT)	07/08/2026 11:21 AM
2W-D-140B	PASS	TIA Cat 6 Perm. Link	161 ft	6.5 dB (NEXT)	07/08/2026 11:22 AM
2W-D-141A	PASS	TIA Cat 6 Perm. Link	161 ft	7.9 dB (NEXT)	07/08/2026 11:05 AM
2W-D-141B	PASS	TIA Cat 6 Perm. Link	161 ft	7.6 dB (NEXT)	07/08/2026 11:06 AM
2W-D-142A	PASS	TIA Cat 6 Perm. Link	167 ft	5.8 dB (NEXT)	07/08/2026 11:02 AM
2W-D-142B	PASS	TIA Cat 6 Perm. Link	168 ft	4.3 dB (NEXT)	07/08/2026 11:03 AM
2W-D-143A	PASS	TIA Cat 6 Perm. Link	174 ft	5.9 dB (NEXT)	07/08/2026 10:57 AM
2W-D-143B	PASS	TIA Cat 6 Perm. Link	173 ft	8.0 dB (NEXT)	07/08/2026 10:58 AM
2W-D-144A	PASS	TIA Cat 6 Perm. Link	179 ft	6.6 dB (NEXT)	07/08/2026 10:54 AM
2W-D-144B	PASS	TIA Cat 6 Perm. Link	179 ft	5.7 dB (NEXT)	07/08/2026 10:54 AM
2W-D-145A	PASS	TIA Cat 6 Perm. Link	135 ft	3.5 dB (NEXT)	07/08/2026 09:31 AM
2W-D-145B	PASS	TIA Cat 6 Perm. Link	135 ft	9.3 dB (NEXT)	07/08/2026 09:32 AM
2W-D-146A	PASS	TIA Cat 6 Perm. Link	171 ft	3.9 dB (NEXT)	07/08/2026 09:19 AM
2W-D-146B	PASS	TIA Cat 6 Perm. Link	171 ft	5.0 dB (NEXT)	07/08/2026 09:20 AM
2W-D-147A	PASS	TIA Cat 6 Perm. Link	171 ft	3.6 dB (NEXT)	07/08/2026 11:15 AM
2W-D-147B	PASS	TIA Cat 6 Perm. Link	171 ft	6.4 dB (NEXT)	07/08/2026 11:16 AM
2W-D-148A	PASS	TIA Cat 6 Perm. Link	165 ft	3.8 dB (NEXT)	07/10/2026 06:44 AM
2W-D-148B	PASS	TIA Cat 6 Perm. Link	165 ft	5.5 dB (NEXT)	07/10/2026 06:45 AM
2W-D-149A	PASS	TIA Cat 6 Perm. Link	159 ft	6.2 dB (NEXT)	07/08/2026 11:09 AM
2W-D-149B	PASS	TIA Cat 6 Perm. Link	160 ft	6.7 dB (NEXT)	07/08/2026 11:10 AM
2W-D-150A	PASS	TIA Cat 6 Perm. Link	154 ft	1.1 dB (NEXT)	07/08/2026 11:08 AM
2W-D-150B	PASS	TIA Cat 6 Perm. Link	153 ft	4.4 dB (NEXT)	07/08/2026 11:08 AM

Total Length:	34510 ft
Number of Reports:	279
Number of Passing Reports:	240
Number of Failing Reports:	39
Number of Warning Reports:	0
Documentation Only:	0

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2W-V-001	FAIL	TIA Cat 6 Perm. Link	145 ft	N/A	07/09/2026 02:52 PM
2W-V-002	PASS	TIA Cat 6 Perm. Link	143 ft	4.3 dB (NEXT)	07/09/2026 02:50 PM
2W-V-003	PASS	TIA Cat 6 Perm. Link	145 ft	4.2 dB (NEXT)	07/09/2026 07:28 AM
2W-V-004	PASS	TIA Cat 6 Perm. Link	144 ft	5.3 dB (NEXT)	07/09/2026 07:21 AM
2W-V-005	PASS	TIA Cat 6 Perm. Link	135 ft	7.4 dB (NEXT)	07/09/2026 07:18 AM
2W-V-006	PASS	TIA Cat 6 Perm. Link	144 ft	4.1 dB (NEXT)	07/09/2026 07:17 AM
2W-V-007	PASS	TIA Cat 6 Perm. Link	135 ft	6.9 dB (NEXT)	07/09/2026 07:15 AM
2W-V-008	FAIL	TIA Cat 6 Perm. Link	134 ft	1.6 dB (NEXT)	07/10/2026 07:50 AM
2W-V-009	FAIL	TIA Cat 6 Perm. Link	140 ft	N/A	07/08/2026 02:49 PM
2W-V-010	FAIL	TIA Cat 6 Perm. Link	145 ft	N/A	07/08/2026 02:45 PM
2W-V-011	FAIL	TIA Cat 6 Perm. Link	97 ft	N/A	07/08/2026 02:42 PM
2W-V-012	PASS	TIA Cat 6 Perm. Link	96 ft	4.2 dB (NEXT)	07/08/2026 02:37 PM
2W-V-013	FAIL	TIA Cat 6 Perm. Link	133 ft	N/A	07/08/2026 02:54 PM
2W-V-014	PASS	TIA Cat 6 Perm. Link	140 ft	5.5 dB (NEXT)	07/09/2026 07:12 AM
2W-V-015	FAIL	TIA Cat 6 Perm. Link	147 ft	N/A	07/08/2026 02:33 PM
2W-V-016	FAIL	TIA Cat 6 Perm. Link	96 ft	N/A	07/08/2026 02:30 PM
2W-V-017	PASS	TIA Cat 6 Perm. Link	99 ft	5.0 dB (NEXT)	07/08/2026 02:27 PM
2W-V-018	PASS	TIA Cat 6 Perm. Link	114 ft	5.1 dB (NEXT)	07/08/2026 02:21 PM
2W-V-019	PASS*	TIA Cat 6 Perm. Link	105 ft	0.3 dB (NEXT)	07/08/2026 02:24 PM
2W-V-020	FAIL	TIA Cat 6 Perm. Link	110 ft	N/A	07/09/2026 07:37 AM
2W-V-021	PASS	TIA Cat 6 Perm. Link	103 ft	8.3 dB (NEXT)	07/09/2026 07:34 AM
2W-V-022	FAIL	TIA Cat 6 Perm. Link	103 ft	N/A	07/09/2026 07:44 AM
2W-V-023	FAIL	TIA Cat 6 Perm. Link	1 ft	N/A	07/09/2026 07:46 AM
2W-V-024	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 07:49 AM
2W-V-025	PASS	TIA Cat 6 Perm. Link	114 ft	6.2 dB (NEXT)	07/09/2026 07:54 AM
2W-V-026	PASS	TIA Cat 6 Perm. Link	156 ft	7.5 dB (NEXT)	07/09/2026 02:43 PM
2W-V-027	FAIL	TIA Cat 6 Perm. Link	97 ft	N/A	07/09/2026 07:57 AM
2W-V-028	PASS	TIA Cat 6 Perm. Link	98 ft	5.4 dB (NEXT)	07/09/2026 08:03 AM
2W-V-029	FAIL	TIA Cat 6 Perm. Link	104 ft	N/A	07/09/2026 08:05 AM
2W-V-030	PASS	TIA Cat 6 Perm. Link	85 ft	7.3 dB (NEXT)	07/09/2026 08:16 AM
2W-V-031	FAIL	TIA Cat 6 Perm. Link	90 ft	N/A	07/09/2026 08:09 AM
2W-V-033	FAIL	TIA Cat 6 Perm. Link	74 ft	N/A	07/09/2026 08:19 AM
2W-V-036	PASS	TIA Cat 6 Perm. Link	53 ft	3.9 dB (NEXT)	07/09/2026 01:30 PM
2W-V-037	PASS	TIA Cat 6 Perm. Link	52 ft	3.9 dB (NEXT)	07/10/2026 07:14 AM
2W-V-038	PASS	TIA Cat 6 Perm. Link	53 ft	2.4 dB (NEXT)	07/09/2026 01:34 PM
2W-V-039	PASS	TIA Cat 6 Perm. Link	90 ft	1.4 dB (NEXT)	07/09/2026 08:34 AM
2W-V-040	FAIL	TIA Cat 6 Perm. Link	85 ft	-0.6 dB (NEXT)	07/09/2026 08:36 AM
2W-V-041	FAIL	TIA Cat 6 Perm. Link	78 ft	N/A	07/09/2026 08:38 AM
2W-V-042	FAIL	TIA Cat 6 Perm. Link	0 ft	N/A	07/09/2026 01:38 PM
2W-V-043	PASS	TIA Cat 6 Perm. Link	64 ft	5.5 dB (NEXT)	07/09/2026 08:50 AM
2W-V-044	PASS	TIA Cat 6 Perm. Link	72 ft	3.5 dB (NEXT)	07/09/2026 08:48 AM
2W-V-045	FAIL	TIA Cat 6 Perm. Link	92 ft	N/A	07/09/2026 08:56 AM
2W-V-046	PASS	TIA Cat 6 Perm. Link	98 ft	5.9 dB (NEXT)	07/09/2026 08:40 AM
2W-V-047	PASS	TIA Cat 6 Perm. Link	103 ft	7.1 dB (NEXT)	07/09/2026 08:44 AM
2W-V-048	PASS	TIA Cat 6 Perm. Link	94 ft	7.6 dB (NEXT)	07/08/2026 02:08 PM
2W-V-050	PASS	TIA Cat 6 Perm. Link	107 ft	6.4 dB (NEXT)	07/08/2026 02:13 PM
2W-V-051	PASS	TIA Cat 6 Perm. Link	114 ft	5.8 dB (NEXT)	07/08/2026 02:16 PM
2W-V-053	PASS	TIA Cat 6 Perm. Link	100 ft	6.1 dB (NEXT)	07/09/2026 01:43 PM
2W-V-054	FAIL	TIA Cat 6 Perm. Link	94 ft	N/A	07/08/2026 02:05 PM
2W-V-055	FAIL	TIA Cat 6 Perm. Link	96 ft	N/A	07/08/2026 01:59 PM
2W-V-056	FAIL	TIA Cat 6 Perm. Link	102 ft	N/A	07/08/2026 01:52 PM
2W-V-057	FAIL	TIA Cat 6 Perm. Link	115 ft	N/A	07/09/2026 02:02 PM
2W-V-058	PASS	TIA Cat 6 Perm. Link	110 ft	5.9 dB (NEXT)	07/09/2026 01:58 PM
2W-V-059	FAIL	TIA Cat 6 Perm. Link	102 ft	N/A	07/09/2026 01:50 PM
2W-V-060	FAIL	TIA Cat 6 Perm. Link	92 ft	N/A	07/09/2026 02:14 PM
2W-V-061	PASS	TIA Cat 6 Perm. Link	98 ft	3.6 dB (NEXT)	07/09/2026 02:11 PM
2W-V-062	FAIL	TIA Cat 6 Perm. Link	105 ft	N/A	07/09/2026 02:09 PM
2W-V-063	PASS	TIA Cat 6 Perm. Link	132 ft	0.9 dB (NEXT)	07/09/2026 03:02 PM
2W-V-064	PASS	TIA Cat 6 Perm. Link	123 ft	4.4 dB (NEXT)	07/09/2026 03:05 PM
2W-V-065	PASS	TIA Cat 6 Perm. Link	114 ft	7.3 dB (NEXT)	07/09/2026 01:25 PM
2W-V-066	PASS	TIA Cat 6 Perm. Link	114 ft	4.5 dB (NEXT)	07/09/2026 01:18 PM
2W-V-067	PASS	TIA Cat 6 Perm. Link	140 ft	2.3 dB (NEXT)	07/09/2026 01:15 PM
2W-V-068	FAIL	TIA Cat 6 Perm. Link	120 ft	N/A	07/09/2026 01:11 PM
2W-V-069	PASS	TIA Cat 6 Perm. Link	152 ft	6.5 dB (NEXT)	07/09/2026 11:08 AM
2W-V-070	FAIL	TIA Cat 6 Perm. Link	151 ft	N/A	07/09/2026 10:56 AM
2W-V-071	FAIL	TIA Cat 6 Perm. Link	146 ft	N/A	07/09/2026 11:09 AM
2W-V-072	FAIL	TIA Cat 6 Perm. Link	165 ft	N/A	07/09/2026 10:42 AM
2W-V-073	PASS	TIA Cat 6 Perm. Link	167 ft	4.7 dB (NEXT)	07/09/2026 10:47 AM
2W-V-074	PASS	TIA Cat 6 Perm. Link	172 ft	4.0 dB (NEXT)	07/09/2026 10:30 AM
2W-V-075	PASS	TIA Cat 6 Perm. Link	171 ft	4.7 dB (NEXT)	07/09/2026 10:35 AM
2W-V-076	PASS	TIA Cat 6 Perm. Link	163 ft	8.4 dB (NEXT)	07/09/2026 10:39 AM
2W-V-077	FAIL	TIA Cat 6 Perm. Link	100 ft	-1.6 dB (NEXT)	07/09/2026 03:10 PM
2W-V-078	PASS	TIA Cat 6 Perm. Link	194 ft	4.2 dB (NEXT)	07/09/2026 09:08 AM
2W-V-079	PASS	TIA Cat 6 Perm. Link	216 ft	6.5 dB (NEXT)	07/09/2026 09:05 AM
2W-V-080	PASS	TIA Cat 6 Perm. Link	208 ft	7.1 dB (NEXT)	07/09/2026 09:15 AM
2W-V-081	PASS*	TIA Cat 6 Perm. Link	216 ft	1.4 dB (NEXT)	07/09/2026 09:56 AM
2W-V-082	PASS	TIA Cat 6 Perm. Link	210 ft	1.4 dB (NEXT)	07/09/2026 10:03 AM
2W-V-083	PASS	TIA Cat 6 Perm. Link	214 ft	4.6 dB (NEXT)	07/09/2026 09:28 AM

Cable ID/ Test ID	Summary	Test Limit	Length	Headroom	Date / Time
2W-V-085	PASS	TIA Cat 6 Perm. Link	216 ft	4.5 dB (NEXT)	07/09/2026 09:30 AM
2W-V-086	PASS	TIA Cat 6 Perm. Link	203 ft	5.2 dB (NEXT)	07/09/2026 09:34 AM
2W-V-087	PASS	TIA Cat 6 Perm. Link	190 ft	3.9 dB (NEXT)	07/09/2026 09:46 AM
2W-V-088	PASS	TIA Cat 6 Perm. Link	198 ft	5.8 dB (NEXT)	07/09/2026 10:05 AM
2W-V-089	PASS	TIA Cat 6 Perm. Link	202 ft	6.3 dB (NEXT)	07/09/2026 09:20 AM
2W-V-090	PASS	TIA Cat 6 Perm. Link	203 ft	5.2 dB (NEXT)	07/09/2026 09:18 AM
2W-V-091	PASS*	TIA Cat 6 Perm. Link	214 ft	0.5 dB (NEXT)	07/09/2026 09:42 AM
2W-V-092	PASS	TIA Cat 6 Perm. Link	224 ft	4.4 dB (NEXT)	07/09/2026 09:39 AM
2W-V-094	PASS	TIA Cat 6 Perm. Link	166 ft	2.0 dB (NEXT)	07/08/2026 01:48 PM
2W-V-095	PASS	TIA Cat 6 Perm. Link	167 ft	3.8 dB (NEXT)	07/09/2026 10:20 AM
2W-V-096	PASS	TIA Cat 6 Perm. Link	166 ft	6.7 dB (NEXT)	07/09/2026 10:18 AM
2W-V-097	PASS	TIA Cat 6 Perm. Link	165 ft	5.7 dB (NEXT)	07/09/2026 10:12 AM
2W-V-098	PASS	TIA Cat 6 Perm. Link	163 ft	4.1 dB (NEXT)	07/09/2026 10:15 AM
2W-V-099	FAIL	TIA Cat 6 Perm. Link	78 ft	N/A	07/08/2026 09:18 AM
2W-V-100	PASS	TIA Cat 6 Perm. Link	91 ft	3.9 dB (NEXT)	07/08/2026 09:20 AM
2W-V-101	PASS	TIA Cat 6 Perm. Link	90 ft	3.1 dB (NEXT)	07/08/2026 09:23 AM
2W-V-102	PASS	TIA Cat 6 Perm. Link	92 ft	3.1 dB (NEXT)	07/08/2026 09:26 AM
2W-V-103	FAIL	TIA Cat 6 Perm. Link	92 ft	N/A	07/08/2026 09:28 AM
2W-V-104	PASS	TIA Cat 6 Perm. Link	85 ft	4.1 dB (NEXT)	07/08/2026 09:33 AM
2W-V-105	FAIL	TIA Cat 6 Perm. Link	85 ft	N/A	07/08/2026 09:35 AM
2W-V-106	PASS	TIA Cat 6 Perm. Link	74 ft	3.4 dB (NEXT)	07/08/2026 09:37 AM
2W-V-107	PASS	TIA Cat 6 Perm. Link	81 ft	3.8 dB (NEXT)	07/08/2026 09:42 AM
2W-V-108	PASS	TIA Cat 6 Perm. Link	83 ft	4.1 dB (NEXT)	07/08/2026 09:45 AM
2W-V-109	FAIL	TIA Cat 6 Perm. Link	93 ft	N/A	07/08/2026 09:58 AM
2W-V-110	FAIL	TIA Cat 6 Perm. Link	99 ft	-1.2 dB (NEXT)	07/08/2026 10:09 AM
2W-V-111	PASS	TIA Cat 6 Perm. Link	106 ft	3.9 dB (NEXT)	07/08/2026 10:12 AM
2W-V-112	PASS	TIA Cat 6 Perm. Link	88 ft	1.6 dB (NEXT)	07/08/2026 09:53 AM
2W-V-113	PASS	TIA Cat 6 Perm. Link	93 ft	3.9 dB (NEXT)	07/08/2026 09:51 AM
2W-V-114	FAIL	TIA Cat 6 Perm. Link	99 ft	N/A	07/08/2026 09:48 AM
2W-V-115	PASS	TIA Cat 6 Perm. Link	135 ft	7.5 dB (NEXT)	07/08/2026 10:05 AM
2W-V-116	PASS	TIA Cat 6 Perm. Link	142 ft	3.8 dB (NEXT)	07/08/2026 10:03 AM
2W-V-117	PASS	TIA Cat 6 Perm. Link	146 ft	2.6 dB (NEXT)	07/08/2026 10:24 AM
2W-V-118	FAIL	TIA Cat 6 Perm. Link	147 ft	N/A	07/08/2026 12:34 PM
2W-V-119	FAIL	TIA Cat 6 Perm. Link	142 ft	N/A	07/08/2026 12:41 PM
2W-V-120	FAIL	TIA Cat 6 Perm. Link	135 ft	N/A	07/08/2026 12:38 PM
2W-V-121	PASS	TIA Cat 6 Perm. Link	98 ft	1.4 dB (NEXT)	07/08/2026 12:59 PM
2W-V-122	PASS	TIA Cat 6 Perm. Link	92 ft	3.8 dB (NEXT)	07/08/2026 12:44 PM
2W-V-123	FAIL	TIA Cat 6 Perm. Link	85 ft	N/A	07/08/2026 12:48 PM
2W-V-124	FAIL	TIA Cat 6 Perm. Link	100 ft	N/A	07/08/2026 12:50 PM
2W-V-125	PASS	TIA Cat 6 Perm. Link	106 ft	1.2 dB (NEXT)	07/08/2026 12:52 PM
2W-V-126	FAIL	TIA Cat 6 Perm. Link	112 ft	N/A	07/08/2026 12:56 PM
2W-V-127	FAIL	TIA Cat 6 Perm. Link	115 ft	N/A	07/08/2026 01:11 PM
2W-V-128	PASS	TIA Cat 6 Perm. Link	122 ft	6.2 dB (NEXT)	07/08/2026 01:14 PM
2W-V-129	PASS	TIA Cat 6 Perm. Link	128 ft	2.8 dB (NEXT)	07/08/2026 01:18 PM
2W-V-130	PASS	TIA Cat 6 Perm. Link	144 ft	3.5 dB (NEXT)	07/08/2026 01:21 PM
2W-V-132	PASS	TIA Cat 6 Perm. Link	156 ft	1.6 dB (NEXT)	07/10/2026 07:37 AM
2W-V-133	PASS	TIA Cat 6 Perm. Link	159 ft	4.3 dB (NEXT)	07/08/2026 01:36 PM
2W-V-134	PASS	TIA Cat 6 Perm. Link	167 ft	5.8 dB (NEXT)	07/08/2026 01:33 PM
2W-V-135	PASS	TIA Cat 6 Perm. Link	171 ft	3.4 dB (NEXT)	07/09/2026 02:25 PM
2W-V-136	PASS	TIA Cat 6 Perm. Link	135 ft	6.1 dB (NEXT)	07/08/2026 12:31 PM
2W-V-137	PASS	TIA Cat 6 Perm. Link	177 ft	4.8 dB (NEXT)	07/08/2026 12:28 PM
2W-V-138	PASS	TIA Cat 6 Perm. Link	172 ft	6.3 dB (NEXT)	07/08/2026 12:26 PM
2W-V-139	PASS	TIA Cat 6 Perm. Link	167 ft	1.1 dB (NEXT)	07/08/2026 12:25 PM
2W-V-140	PASS	TIA Cat 6 Perm. Link	160 ft	7.4 dB (NEXT)	07/08/2026 12:21 PM
2W-V-141	PASS	TIA Cat 6 Perm. Link	160 ft	6.6 dB (NEXT)	07/08/2026 12:05 PM
2W-V-142	PASS	TIA Cat 6 Perm. Link	167 ft	4.3 dB (NEXT)	07/08/2026 12:01 PM
2W-V-143	PASS	TIA Cat 6 Perm. Link	172 ft	5.9 dB (NEXT)	07/08/2026 11:56 AM
2W-V-144	PASS	TIA Cat 6 Perm. Link	179 ft	5.8 dB (NEXT)	07/08/2026 11:53 AM
2W-V-145	FAIL	TIA Cat 6 Perm. Link	134 ft	N/A	07/08/2026 10:31 AM
2W-V-146	PASS	TIA Cat 6 Perm. Link	169 ft	1.3 dB (NEXT)	07/08/2026 10:19 AM
2W-V-147	PASS	TIA Cat 6 Perm. Link	169 ft	4.2 dB (NEXT)	07/08/2026 12:15 PM
2W-V-148	PASS	TIA Cat 6 Perm. Link	162 ft	5.6 dB (NEXT)	07/10/2026 07:44 AM
2W-V-149	PASS	TIA Cat 6 Perm. Link	157 ft	3.8 dB (NEXT)	07/08/2026 12:10 PM
2W-V-150	PASS	TIA Cat 6 Perm. Link	150 ft	2.6 dB (NEXT)	07/08/2026 12:08 PM

Total Length:	18067 ft
Number of Reports:	142
Number of Passing Reports:	96
Number of Failing Reports:	46
Number of Warning Reports:	0
Documentation Only:	0
